

**GRANT AGREEMENT BETWEEN THE STATE OF CALIFORNIA
(DEPARTMENT OF WATER RESOURCES) AND
COACHELLA VALLEY WATER DISTRICT
AGREEMENT NUMBER 4600014978
PROPOSITION 1 ROUND 2 INTEGRATED REGIONAL WATER MANAGEMENT (IRWM)
IMPLEMENTATION GRANT
AMENDMENT 2**

THIS GRANT AGREEMENT is entered into by and between the Department of Water Resources of the State of California, herein referred to as the "State" or "DWR," and the Coachella Valley Water District, a Public Agency in the State of California, duly organized, existing, and acting pursuant to the laws thereof, herein referred to as the "Grantee," which parties do hereby agree as follows:

- 1) **PURPOSE.** The State shall provide funding from the Water Quality, Supply, and Infrastructure Improvement Act of 2014 (Proposition 1) to the Grantee to assist in financing the projects, which are included in and implemented in an adopted Integrated Regional Water Management Plan (IRWM Plan), pursuant to Chapter 7. Regional Water Security, Climate, and Drought Preparedness (Wat. Code, § 79740 et seq.). The provision of State funds pursuant to this Agreement shall be construed or interpreted to mean that the IRWM Plan, or any components of the IRWM Plan, implemented in accordance with the Work Plan as set forth in Exhibit A, has been adopted through the IRWM Plan Review Process, and is/are consistent with Water Code section 10530 et seq.
- 2) **TERM OF GRANT AGREEMENT.** The term of this Grant Agreement begins on November 23, 2022, through final payment plus three (3) years unless otherwise terminated or amended as provided in this Grant Agreement. However, all work shall be completed by March 31, 2027, in accordance with the Schedule as set forth in Exhibit C and no funds may be requested after June 30, 2027.
- 3) **GRANT AMOUNT.** The maximum amount payable by the State under this Grant Agreement shall not exceed \$4,112,755.
- 4) **GRANTEE COST SHARE.** The Grantee is required to provide a Local Cost Share (non-state funds) as set forth in Exhibit B (Budget). Local Cost Share may include Eligible Project Costs directly related to Exhibit A incurred after January 1, 2015.
- 5) **BASIC CONDITIONS.** The State shall have no obligation to disburse money for the Project(s) under this Grant Agreement until the Grantee has satisfied the following conditions (if applicable):
 - A. The Grantee shall demonstrate compliance with all eligibility criteria as set forth on pages 9-11, inclusive, of the 2022 IRWM Grant Program Guidelines (2022 Guidelines).
 - B. For the term of this Agreement, the Grantee shall submit Quarterly Progress Reports which must accompany an invoice and all invoice backup documentation (\$0 Invoices are acceptable). The Quarterly Progress Report shall be submitted within 60 days following the end of the calendar quarter (i.e. reports due May 30, August 29, November 29, and March 1) and all other deliverables as required by Paragraph 14, "Submission of Reports" and Exhibit A, "Work Plan".
 - C. Prior to the commencement of construction or implementation activities, if applicable, the Grantee shall submit the following to the State.
 - i. Final plans and specifications certified, signed and stamped by a California Registered Civil Engineer (or equivalent registered professional as appropriate) to certify compliance for each approved project as listed in Exhibit A of this Grant Agreement.
 - ii. Work that is subject to the California Environmental Quality Act (CEQA) (including final land purchases) shall not proceed under this Grant Agreement until the following actions are performed:

- a) The Grantee submits to the State all applicable environmental permits, as indicated on the Environmental Information Form to the State,
- b) All documents that satisfy the CEQA process are received by the State,
- c) The State has completed its CEQA process as a Responsible Agency, and
- d) The Grantee receives written notification from the State of concurrence with the Lead Agency's CEQA documents (s) and State's notice of verification of environmental permit submittal.

The State's concurrence of Lead Agency's CEQA documents is fully discretionary and shall constitute a condition precedent to any work (i.e., construction or implementation activities) for which it is required. Once CEQA documentation has been completed, the State will consider the environmental documents and decide whether to continue to fund the project, or to require changes, alterations, or other mitigation. Proceeding with work subject to CEQA prior to the State's concurrence shall constitute a material breach of this Agreement. The Grantee or Local Project Sponsor (LPS) shall also demonstrate that it has complied with all applicable requirements of the National Environmental Policy Act (NEPA) by submitting copies of any environmental documents, including Environmental Impact Statements, Finding of No Significant Impact, mitigation monitoring programs, and environmental permits as may be required prior to beginning construction/ implementation.

iii. A monitoring plan as required by Paragraph 16, "Monitoring Plan Requirements," if applicable.

- 6) DISBURSEMENT OF FUNDS. The State will disburse to the Grantee the amount approved, subject to the availability of funds through normal State processes. Notwithstanding any other provision of this Grant Agreement, no disbursement shall be required at any time or in any manner which is in violation of, or in conflict with, federal or state laws, rules, or regulations, or which may require any rebates to the federal government, or any loss of tax-free status on state bonds, pursuant to any federal statute or regulation. Any and all money disbursed to the Grantee under this Grant Agreement shall be deposited in a non-interest bearing account and shall be used solely to pay Eligible Project Costs.
- 7) ELIGIBLE PROJECT COST. The Grantee shall apply State funds received only to Eligible Project Costs in accordance with applicable provisions of the law and Exhibit B, "Budget". Eligible Project Costs include the reasonable costs of studies, engineering, design, land and easement acquisition and associated legal fees, preparation of environmental documentation, environmental mitigations, monitoring, and project construction. Reimbursable administrative expenses are the necessary costs incidental but directly related to the Project included in this Agreement. Costs incurred after November 22, 2022, may be eligible for reimbursement.

Costs that are not eligible for reimbursement include, but are not limited to, the following items:

- A. Costs, other than those noted above, incurred prior to the award date of this Grant.
- B. Costs for preparing and filing a grant application.
- C. Operation and maintenance costs, including post construction performance and monitoring costs.
- D. Purchase of equipment that is not an integral part of a project.
- E. Establishing a reserve fund.
- F. Purchase of water supply.
- G. Replacement of existing funding sources (e.g., bridge loans).
- H. Meals, food items, or refreshments.
- I. Payment of any punitive regulatory agency requirement, federal or state taxes.

- J. Purchase of land in excess of the minimum required acreage necessary to operate as an integral part of a project, as set forth and detailed by engineering and feasibility studies, or acquisition of land by eminent domain.
- K. Indirect Costs. "Indirect Costs" means those costs that are incurred for a common or joint purpose benefiting more than one cost objective and are not readily assignable to the funded project (i.e., costs that are not directly related to the funded project). Examples of Indirect Costs include but are not limited to: central service costs; general administration of the Grantee or LPSs; non-project-specific accounting and personnel services performed within the Grantee's or LPS' organization; depreciation or use allowances on buildings and equipment; the costs of operating and maintaining non-project-specific facilities; tuition and conference fees; forums, trainings, and seminars; and, generic overhead or markup. This prohibition applies to the Grantee, LPSs, and any subcontract or sub-agreement for work on the Project that will be reimbursed pursuant to this Agreement.
- L. Mitigation for environmental impacts not resulting from implementation of the Project funded by this program.
- M. Costs incurred as part of any necessary response and cleanup activities required under the Comprehensive Environmental Response, Compensation, and Liability Act; Resource Conservation and Recovery Act; Hazardous Substances Account Act; or other applicable law.
- 8) **METHOD OF PAYMENT.** After the disbursement requirements in Paragraph 5, "Basic Conditions" are met, the State will disburse the whole or portions of State funding to the Grantee, following receipt from the Grantee of an electronic invoice certified and transmitted via electronic/digital signature system (e.g., DocuSign) or via US mail or Express mail delivery of a "wet signature" for costs incurred, including Local Cost Share, and timely Quarterly Progress Reports as required by Paragraph 14, "Submission of Reports." Payment will be made no more frequently than quarterly, in arrears, upon receipt of an invoice bearing the Grant Agreement number. Quarterly Progress Report must accompany an invoice (\$0 Invoices are acceptable) and shall be submitted within 60 days following the end of the calendar quarter (i.e., invoices due May 30, August 29, November 29, and March 1). The State will notify the Grantee, in a timely manner, whenever, upon review of an invoice, the State determines that any portion or portions of the costs claimed are not eligible costs or is not supported by documentation or receipts acceptable to the State. The Grantee may, within thirty (30) calendar days of the date of receipt of such notice, submit additional documentation to the State to cure such deficiency(ies). If the Grantee fails to submit adequate documentation curing the deficiency(ies), the State will adjust the pending invoice by the amount of ineligible or unapproved costs.

Invoices submitted by the Grantee shall include the following information:

- A. Costs incurred for work performed in implementing the Project during the period identified in the particular invoice.
- B. Costs incurred for any interests in real property (land or easements) that have been necessarily acquired for a project during the period identified in the particular invoice for the implementation of a project.
- C. Invoices shall be submitted on forms provided by the State and shall meet the following format requirements:
- i. Invoices shall contain the date of the invoice, either the time period covered by the invoice or the invoice date received within the time period covered, and the total amount due.
 - ii. Invoices shall be itemized based on the categories (i.e., tasks) specified in Exhibit B, "Budget." The amount claimed for salaries/wages/consultant fees shall include a calculation formula (i.e., hours or days worked times the hourly or daily rate = the total amount claimed).

- iii. One set of sufficient evidence (i.e., receipts, copies of checks, personnel hours' summary table, time sheets) shall be provided for all costs included in the invoice.
- iv. Each invoice shall clearly delineate those costs claimed for reimbursement from the State's funding amount, as depicted in Paragraph 3, "Grant Amount" and those costs that represent the Grantee's costs, as applicable, in Paragraph 4, "Grantee Cost Share."
- v. Original signature and date of the Grantee's Project Representative. Submit an electronic invoice, certified and transmitted via electronic/digital signature system (e.g., DocuSign), from authorized representative to the Project Manager or the original "wet signature" copy of the invoice form to the Project Manager at the following address: Financial Assistance Branch, DWR, P.O. Box 942836, Sacramento, CA 94236.

All invoices submitted shall be accurate and signed under penalty of law. Any and all costs submitted pursuant to this Agreement shall only be for the tasks set forth herein. The Grantee shall not submit any invoice containing costs that are ineligible or have been reimbursed from other funding sources unless required and specifically noted as such (i.e., cost share). Any eligible costs for which the Grantee is seeking reimbursement shall not be reimbursed from any other source. Double or multiple billing for time, services, or any other eligible cost is illegal and constitutes fraud. Any suspected occurrences of fraud, forgery, embezzlement, theft, or any other misuse of public funds may result in suspension of disbursements of grant funds and/or termination of this Agreement requiring the repayment of all funds disbursed hereunder plus interest. Additionally, the State may request an audit pursuant to Standard Condition D.5 and refer the matter to the Attorney General's Office or the appropriate district attorney's office for criminal prosecution or the imposition of civil liability. (Civ. Code, §§ 1572-1573; Pen. Code, §§ 470, 487-489.)

- 9) ADVANCED PAYMENT. Water Code section 10551 authorizes advanced payment by the State for projects included and implemented in an applicable Integrated Regional Water Management Plan, and when the project proponent is a nonprofit organization; a disadvantaged community (DAC); or the project benefits a DAC. If a project is awarded less than \$1,000,000 in grant funds, the project proponent may receive an advanced payment of fifty (50) percent of the grant award; the remaining fifty (50) percent of the grant award will be reimbursed in arrears after the advanced funds of a budget category have been fully expended. Within ninety (90) calendar days of execution of the Grant Agreement, the Grantee may provide the State an Advanced Payment Request. Advanced Payment Requests received ninety-one (91) calendar days after the execution of this Agreement will not be eligible to receive an advanced payment. The Advanced Payment Request shall contain the following:
- A. Documentation demonstrating that each Local Project Sponsor (if different from the Grantee, as listed in Exhibit I) was notified about their eligibility to receive an advanced payment and a response from the Local Project Sponsor stating whether it wishes to receive the advanced payment or not.
 - B. If the Grantee is requesting the advanced payment, the request(s) shall include:
 - i. Descriptive information of each project with an update on project status
 - ii. The names of the entities that will receive the funding for each project, including, but not limited to, an identification as to whether the project proponent or proponents are nonprofit organizations or a DAC, or whether the project benefits a DAC
 - iii. A detailed Funding Plan which includes how the advanced payment will be expended (in terms of workplan, budget, and schedule) within the timeframe agreed upon by DWR and the Grantee. The Funding Plan must clearly identify the total budget (at Budget Category Level) for each project clearly showing the portion of advanced payment and reimbursement funds.
 - iv. Any other information that DWR may deem necessary

- C. Upon review and approval of the Advanced Payment Request, DWR will authorize payment of the fully requested amount for the qualified project(s). Based on the project's Funding Plan and other considerations, DWR may determine it is not prudent to advance the full request in a single disbursement. In such a case, DWR will develop a "Disbursement Schedule," to disburse funds in installments. This Disbursement Schedule may change based on the project's ongoing compliance with the Advanced Payment requirements and the project's cash flow needs.
- D. Once DWR authorizes the Advanced Payment Request, the Grantee shall submit Advanced Payment Invoice(s) for the initial amount based on the "Disbursement Schedule" on behalf of the LPS(s), containing the request for each qualified project, to the State with signature and date of the Grantee's Project Representative, as indicated in Paragraph 21, "Project Representative." The Grantee shall be responsible for the timely distribution of the advanced funds to the respective LPS(s). The Advanced Payment Invoice(s) shall be submitted on forms provided by the State and shall meet the following format requirements:
- i. Invoice shall contain the date of the invoice, the time period covered by the invoice, and the total amount due.
 - ii. Invoice shall be itemized based on the budget categories specified in Exhibit B, "Budget."
 - iii. The State Project Manager will notify the Grantee, in a timely manner, when, upon review of an Advance Payment Invoice, the State determines that any portion or portions of the costs claimed are not eligible costs. The Grantee may, within thirty (30) calendar days of the date of receipt of such notice, submit additional documentation to cure such deficiency(ies).
 - iv. On a quarterly basis, the Grantee will submit an Accountability Report to the State that demonstrates how actual expenditures compare with the scheduled budget. The Accountability Report shall include the following information:
 1. An itemization of how advanced funds have been spent to-date (Expenditure Report), including documentation that supports the disbursements (e.g., contractor invoices, receipts, personnel hours, etc.). Accountability Reports shall be itemized based on the budget categories (i.e., tasks) specified in Exhibit B.
 2. An updated Accountability Report including an updated Funding Plan that depicts how the remaining advanced funds will be expended and the activities and deliverables associated with the advanced funds within the timeframe agreed upon by DWR and the Grantee when the advanced payment request was approved.
 3. Documentation that the funds were placed in a non-interest bearing account, including the dates of deposits and withdrawals from that account.
 4. Proof of distribution of advanced funds to LPS(s), if applicable.
 - v. The State's Project Manager will notify the Grantee, in a timely manner, when, upon review of the Accountability Report, the State determines that any portion of the expenditures claimed are not eligible costs. The Grantee may, within thirty (30) calendar days of the date of receipt of such notice, submit additional documentation to cure such deficiency(ies). If costs are not consistent with the tasks in Exhibit A, the State will reject the claim and remove them from the Accountability Report.
- E. Once the Grantee has spent all advanced funds in a budget category, then the method of payment will revert to the reimbursement process for that budget category specified in Paragraph 8, "Method of Payment for Reimbursement."
- 10) REPAYMENT OF ADVANCES. The State may demand repayment from the Grantee of all or any portion of the advanced State funding along with interest at the California general obligation bond interest rate at

the time the State notifies the Grantee, as directed by the State, and take any other action that it deems necessary to protect its interests for the following conditions:

- A. A project is not being implemented in accordance with the provisions of the Grant Agreement.
- B. The Grantee has failed in any other respect to comply with the provisions of this Grant Agreement, and if the Grantee does not remedy any such failure to the State's satisfaction.
- C. Failure by the Grantee to submit complete and accurate quarterly Accountability Reports by the required due dates, unless otherwise approved by DWR.
- D. Failure to deposit funds in a non-interest-bearing account.
- E. Use of Advance Payment funds for ineligible expenses and/or activities not consistent with this Agreement.
- F. Inappropriate use of funds, as deemed by DWR.
- G. Repayment amounts may also include:
 - i. Actual costs incurred which are not consistent with the activities presented in Exhibit A, not supported, or are ineligible.
 - ii. Advanced funds which are not fully expended by project completion, notwithstanding Water Code section 10551(c)(4). Unused grant funds shall be returned to DWR within sixty (60) calendar days.

Any repayment of advanced funds may consist of reducing the amount from future reimbursement invoices. The State may consider the Grantee's refusal to repay the requested advanced amount a material breach of this Agreement subject to the default provisions in Paragraph 12, "Default Provisions." If the State notifies the Grantee of its decision to demand repayment or withhold the entire funding amount from the Grantee pursuant to this Paragraph, this Grant Agreement shall terminate upon receipt of such notice by the Grantee and the State shall no longer be required to provide funds under this Agreement.

11) WITHHOLDING OF DISBURSEMENTS BY THE STATE. If the State determines that a project is not being implemented in accordance with the provisions of this Grant Agreement, or that the Grantee has failed in any other respect to comply with the provisions of this Grant Agreement, and if the Grantee does not remedy any such failure to the State's satisfaction, the State may withhold from the Grantee all or any portion of the State funding and take any other action that it deems necessary to protect its interests. Where a portion of the State funding has been disbursed to the Grantee and the State notifies the Grantee of its decision not to release funds that have been withheld pursuant to Paragraph 12, "Default Provisions," the portion that has been disbursed shall thereafter be repaid immediately with interest at the California general obligation bond interest rate at the time the State notifies the Grantee, as directed by the State. The State may consider the Grantee's refusal to repay the requested disbursed amount a material breach subject to the default provisions in Paragraph 12, "Default Provisions." If the State notifies the Grantee of its decision to withhold the entire funding amount from the Grantee pursuant to this Paragraph, this Grant Agreement shall terminate upon receipt of such notice by the Grantee and the State shall no longer be required to provide funds under this Grant Agreement and the Grant Agreement shall no longer be binding on either party.

12) DEFAULT PROVISIONS. The Grantee shall be in default under this Grant Agreement if any of the following occur:

- A. Substantial breaches of this Grant Agreement, or any supplement or amendment to it, or any other Agreement between the Grantee and the State evidencing or securing the Grantee's obligations.
- B. Making any false warranty, representation, or statement with respect to this Grant Agreement or the application filed to obtain this Grant Agreement.
- C. Failure to operate or maintain the Project in accordance with this Grant Agreement.

- D. Failure to make any remittance required by this Grant Agreement, including any remittance recommended as the result of an audit conducted pursuant to Standard Condition D.5.
- E. Failure to submit quarterly progress reports pursuant to Paragraph 5.
- F. Failure to routinely invoice the State pursuant to Paragraph 8.
- G. Failure to meet any of the requirements set forth in Paragraph 13, "Continuing Eligibility."

Should an event of default occur, the State shall provide a notice of default to the Grantee and shall give the Grantee at least ten (10) calendar days to cure the default from the date the notice is sent via first-class mail to the Grantee. If the Grantee fails to cure the default within the time prescribed by the State, the State may do any of the following:

- A. Declare the funding be immediately repaid, with interest, which shall be equal to State of California general obligation bond interest rate in effect at the time of the default.
- B. Terminate any obligation to make future payments to the Grantee.
- C. Terminate the Grant Agreement.
- D. Take any other action that it deems necessary to protect its interests.

In the event the State finds it necessary to enforce this provision of this Grant Agreement in the manner provided by law, the Grantee agrees to pay all costs incurred by the State including, but not limited to, reasonable attorneys' fees, legal expenses, and costs.

- 13) CONTINUING ELIGIBILITY. The Grantee shall meet the following ongoing requirement(s) and all eligibility criteria outlined in the 2022 Guidelines to remain eligible to receive State funds:
- A. An urban water supplier that receives grant funds pursuant to this Agreement shall maintain compliance with the Urban Water Management Planning Act (UWMP; Wat. Code, § 10610 et seq.) and Sustainable Water Use and Demand Reduction (Wat. Code, § 10608 et seq.) as set forth on page 11 of the 2022 Guidelines and as stated on pages 24-25 of the 2022 IRWM Implementation Grant Proposal Solicitation Package.
 - B. An agricultural water supplier receiving grant funds shall comply with Sustainable Water Use and Demand Reduction requirements outlined in Water Code section 10608, et seq. and have their Agricultural Water Management Plan (AWMP) deemed consistent by DWR. To maintain eligibility and continue funding disbursements, an agricultural water supply shall have their 2015 AWMP identified on the State's website. For more information, visit the website listed in Appendix A in the 2022 Guidelines.
 - C. A surface water diverter receiving grant funds shall maintain compliance with diversion reporting requirements as outlined in Water Code section 5100 et. seq.
 - D. If applicable, the Grantee shall demonstrate compliance with the Sustainable Groundwater Management Act (SGMA) set forth on page 10 of the 2022 Guidelines.
 - E. If the Grantee has been designated as a monitoring entity under the California Statewide Groundwater Elevation Monitoring (CASGEM) Program, the Grantee shall maintain reporting compliance, as required by Water Code section 10932 and the CASGEM Program.
 - F. The Grantee shall adhere to the protocols developed pursuant to The Open and Transparent Water Data Act (Wat. Code, § 12406, et seq.) for data sharing, transparency, documentation, and quality control.
 - G. On March 4, 2022, the Governor issued Executive Order N-6-22 (the EO) regarding Economic Sanctions against Russia and Russian entities and individuals. The EO may be found at: <https://www.gov.ca.gov/wp-content/uploads/2022/03/3.4.22-Russia-Ukraine-Executive-Order.pdf>.

“Economic Sanctions” refers to sanctions imposed by the U.S. government in response to Russia’s actions in Ukraine, as well as any sanctions imposed under State law. The EO directs DWR to terminate funding agreements with, and to refrain from entering any new agreements with, individuals or entities that are determined to be a target of Economic Sanctions. Accordingly, should the State determine that the Grantee is a target of Economic Sanctions or is conducting prohibited transactions with sanctioned individuals or entities, that shall be grounds for termination of this Agreement. The State shall provide the Grantee advance written notice of such termination, allowing the Grantee at least 30 calendar days to provide a written response. Termination shall be at the sole discretion of the State.

- 14) SUBMISSION OF REPORTS. The submittal and approval of all reports is a requirement for the successful completion of this Grant Agreement. Reports shall meet generally accepted professional standards for technical reporting and shall be proofread for content, numerical accuracy, spelling, and grammar prior to submittal to the State. All reports shall be submitted to the State’s Project Manager and shall be submitted via the DWR “Grant Review and Tracking System” (GRanTS). If requested, the Grantee shall promptly provide any additional information deemed necessary by the State for the approval of reports. Reports shall be presented in the formats described in the applicable portion of Exhibit F, “Report Formats and Requirements.” The timely submittal of reports is a requirement for initial and continued disbursement of State funds. Submittal and subsequent approval by the State of a Project Completion Report is a requirement for the release of any funds retained for such project.
- A. Quarterly Progress Reports: The Grantee shall submit quarterly Progress Reports to meet the State’s requirement for disbursement of funds. Progress Reports shall be uploaded via GRanTS, and the State’s Project Manager notified of upload. Progress Reports shall, in part, provide a brief description of the work performed, the Grantee’s activities, milestones achieved, any accomplishments and any problems encountered in the performance of the work under this Grant Agreement during the reporting period. The first Progress Report must accompany an invoice (\$0 Invoices are acceptable) and shall be submitted within 60 days following the end of the calendar quarter (i.e. invoices due May 30, August 29, November 29, and March 1).
 - B. Accountability Report: The Grantee shall prepare and submit to the State an Accountability Report on a quarterly basis if the Grantee received an advanced payment, consistent with the provisions in Paragraph 9, “Advanced Payment.”
 - C. Project Completion Report: The Grantee shall prepare and submit to the State a separate Project Completion Report for each project included in Exhibit A. The Grantee shall submit a Project Completion Report (or a Component Completion Report, if a Project has multiple Components) within ninety (90) calendar days of Project/Component completion as outlined in Exhibit F.
 - D. Grant Completion Report: Upon completion of all the Projects included in Exhibit A, the Grantee shall submit to the State a Grant Completion Report. The Grant Completion Report shall be submitted within ninety (90) calendar days of submitting the Completion Report for the final project to be completed under this Grant Agreement, as outlined in Exhibits A, and F. Retention for any grant administration line items in the Budget of this Grant Agreement will not be disbursed until the Grant Completion Report is approved by the State.
 - E. Post-Performance Reports: The Grantee shall prepare and submit to the State Post-Performance Reports for the applicable project(s). Post-Performance Reports shall be submitted to the State within ninety (90) calendar days after the first operational year of a project has elapsed. This record keeping and reporting process shall be repeated annually for a total of three (3) years after the project begins operation.
- 15) OPERATION AND MAINTENANCE OF PROJECT. For the useful life of construction and implementation projects and in consideration of the funding made by the State, the Grantee agrees to ensure or cause to be performed the commencement and continued operation of the project, and shall ensure or cause the

project to be operated in an efficient and economical manner; shall ensure all repairs, renewals, and replacements necessary to the efficient operation of the same are provided; and shall ensure or cause the same to be maintained in as good and efficient condition as upon its construction, ordinary and reasonable wear and depreciation excepted. The State shall not be liable for any cost of such maintenance, management, or operation. The Grantee or their successors may, with the written approval of the State, transfer this responsibility to use, manage, and maintain the property. For purposes of this Grant Agreement, "useful life" means period during which an asset, property, or activity is expected to be usable for the purpose it was acquired or implemented; "operation costs" include direct costs incurred for material and labor needed for operations, utilities, insurance, and similar expenses, and "maintenance costs" include ordinary repairs and replacements of a recurring nature necessary for capital assets and basic structures and the expenditure of funds necessary to replace or reconstruct capital assets or basic structures. Refusal by the Grantee to ensure operation and maintenance of the projects in accordance with this provision may, at the option of the State, be considered a breach of this Grant Agreement and may be treated as default under Paragraph 12, "Default Provisions."

- 16) MONITORING PLAN REQUIREMENTS. A Monitoring Plan shall be submitted to the State prior to disbursement of State funds for construction or monitoring activities. The Monitoring Plan should incorporate Post-Performance Monitoring Report requirements as defined and listed in Exhibit F, and follow the guidance provided in Exhibit L, "Project Monitoring Plan Guidance."
- 17) STATEWIDE MONITORING REQUIREMENTS. The Grantee shall ensure that all groundwater projects and projects that include groundwater monitoring requirements are consistent with the Groundwater Quality Monitoring Act of 2001 (Water Code § 10780 et seq.) and, where applicable, that projects that affect water quality shall include a monitoring component that allows the integration of data into statewide monitoring efforts, including where applicable, the Surface Water Ambient Monitoring Program carried out by the State Water Resources Control Board. See Exhibit G for web links and information regarding other State monitoring and data reporting requirements.
- 18) NOTIFICATION OF STATE. The Grantee shall promptly notify the State, in writing, of the following items:
 - A. Events or proposed changes that could affect the scope, budget, or work performed under this Grant Agreement. The Grantee agrees that no substantial change in the scope of a project will be undertaken until written notice of the proposed change has been provided to the State and the State has given written approval for such change. Substantial changes generally include changes to the scope of work, schedule or term, and budget.
 - B. Any public or media event publicizing the accomplishments and/or results of this Grant Agreement and provide the opportunity for attendance and participation by the State's representatives. Grantee shall make such notification at least fourteen (14) calendar days prior to the event.
 - C. Discovery of any potential archaeological or historical resource. Should a potential archaeological or historical resource be discovered during construction, the Grantee agrees that all work in the area of the find shall cease until a qualified archaeologist has evaluated the situation and made recommendations regarding preservation of the resource, and the State has determined what actions should be taken to protect and preserve the resource. The Grantee agrees to implement appropriate actions as directed by the State.
 - D. The initiation of any litigation or the threat of litigation against the Grantee or an LPS regarding the Project or which may affect the Project in any way.
 - E. Applicable to construction projects only: Final inspection of the completed work on a project by a Registered Professional (Civil Engineer, Engineering Geologist, or other State approved certified/licensed Professional), in accordance with Exhibit D. The Grantee shall notify the State's Project Manager of the inspection date at least fourteen (14) calendar days prior to the inspection in order to provide the State the opportunity to participate in the inspection.

- 19) NOTICES. Any notice, demand, request, consent, or approval that either party desires or is required to give to the other party under this Grant Agreement shall be in writing. Notices may be transmitted by any of the following means:
- A. By delivery in person.
 - B. By certified U.S. mail, return receipt requested, postage prepaid.
 - C. By “overnight” delivery service; provided that next-business-day delivery is requested by the sender.
 - D. By electronic means.
 - E. Notices delivered in person will be deemed effective immediately on receipt (or refusal of delivery or receipt). Notices sent by certified mail will be deemed effective given ten (10) calendar days after the date deposited with the U.S. Postal Service. Notices sent by overnight delivery service will be deemed effective one business day after the date deposited with the delivery service. Notices sent electronically will be effective on the date of transmission, which is documented in writing. Notices shall be sent to the addresses listed below. Either party may, by written notice to the other, designate a different address that shall be substituted for the one below.
- 20) PERFORMANCE EVALUATION. Upon completion of this Grant Agreement, the Grantee’s performance will be evaluated by the State and a copy of the evaluation will be placed in the State file and a copy sent to the Grantee.
- 21) PROJECT REPRESENTATIVES. The Project Representatives during the term of this Grant Agreement are as follows:

Department of Water Resources

Arthur Hinojosa
Manager, Division of Regional Assistance
P.O. Box 942836
Sacramento, CA 94236
Phone: (916) 902-6713
Email: Arthur.Hinojosa@water.ca.gov

Coachella Valley Water District

J.M. Barrett
General Manager
P.O. Box 1058
Coachella, CA 92236
Phone: (760) 398-2661
Email: jbarrett@cvwd.org

Direct all inquiries to the Project Manager:

Department of Water Resources

Faiyaz Mohammed
Engineer, Water Resources
Division of Regional Assistance
P.O. Box 942836
Sacramento, CA 94236-0001
Phone: (916) 326-9951
email: Faiyaz.mohammed@water.ca.gov

Coachella Valley Water District

David Lacy
Finance Manager
P.O. Box 1058,
Coachella, CA 92236
Phone: (760) 398-2661
Email: dlacy@cvwd.org

Either party may change its Project Representative or Project Manager upon written notice to the other party.

22) STANDARD PROVISIONS. This Grant Agreement is complete and is the final Agreement between the parties. The following Exhibits are attached and made a part of this Grant Agreement by this reference:

Exhibit A – Work Plan

Exhibit B – Budget

Exhibit C – Schedule

Exhibit D – Standard Conditions

Exhibit E – Authorizing Resolution

Exhibit F – Report Formats and Requirements

Exhibit G – Requirements for Data Submittal

Exhibit H – State Audit Document Requirements and Cost Share Guidelines for the Grantee

Exhibit I – Local Project Sponsors and Project Locations

Exhibit J – Appraisal Specifications

Exhibit K – Information Needed for Escrow Processing and Closure


Exhibit L – Project Monitoring Plan Guidance

Exhibit M – Invoice Guidance for Administrative and Overhead Charges


IN WITNESS WHEREOF, the parties hereto have executed this Grant Agreement.

STATE OF CALIFORNIA
DEPARTMENT OF WATER RESOURCES

COACHELLA VALLEY WATER
DISTRICT



Arthur Hinojosa
Manager, Division of Regional Assistance



J.M. Barrett
General Manager

Date 4/3/2025

Date 4/3/2025

EXHIBIT A
WORK PLAN**PROPOSITION 1 ROUND 2 COACHELLA VALLEY IRWM IMPLEMENTATION GRANT****PROJECT 1: Grant Administration****IMPLEMENTING AGENCY:** Coachella Valley Water District (Grantee)**PROJECT DESCRIPTION:** The Grantee will administer these funds and respond to DWR's reporting and compliance requirements associated with the grant administration. This Grantee will act in a coordination role: disseminating grant compliance information to the project managers responsible for implementing the projects contained in this agreement, obtaining and retaining evidence of compliance (e.g., CEQA/NEPA documents, reports, monitoring compliance documents, labor requirements, etc.), obtaining data for progress reports from individual project managers, assembling and submitting progress reports to the State, and coordinating all invoicing and payment of invoices.**Budget Category (a): Project Administration**Task 1: Agreement Administration

The Grantee will respond to DWR's reporting and compliance requirements associated with the grant administration and will coordinate with the project managers responsible for implementing the projects contained in this agreement.

Task 2: Invoicing

The Grantee will be responsible for compiling invoices for submittal to DWR. This includes collecting invoice documentation from each of the Local Project Sponsors and compiling the information into a DWR Invoice Packet.

Deliverables:

- Quarterly Invoices and associated backup documentation
- Advanced Payment documentation as per Paragraph 9 (if applicable)

Task 3: Reporting

The Grantee will be responsible for compiling progress reports for submittal to DWR. The Grantee will coordinate with Local Project Sponsor staff to retain consultants as needed to prepare and submit progress reports and final project completion reports for each project, as well as the grant completion report.

Reports will meet generally accepted professional standards for technical reporting and the requirements terms of the contract with DWR outlined in Exhibit F of this Agreement.

Deliverables:

- Quarterly Progress Reports
- Grant Completion Report

PROJECT 1: Reservoirs 4711-3 and 4711-4 Construction Project

Amendment 2: Project 1 Removed and Replaced with Project 7

PROJECT 2: Desert Water Agency Regional Conservation Program

IMPLEMENTING AGENCY: Desert Water Agency (DWA)

PROJECT DESCRIPTION: The project includes the components described below that are all implemented under the regional program and will conserve approximately 57 acre-feet per year (AFY) of water, reducing the region's dependence on groundwater:

Regional Grass Replacement Program: The Regional Grass Replacement Program is a multifaceted program that will make turf rebates available throughout the Coachella Valley Water Management Group's (CVRWVG) collective service area for a variety of water customers, including residential and multi-family sites. This program will assist the Region's water purveyors in effectively managing groundwater by reducing demands and groundwater pumping. Additionally, grass removal includes the removal of sprinklers in favor of drip irrigation or no irrigation. This results in less pesticide and fertilizer application and less dry weather urban runoff.

Smart Irrigation Controller Rebate Program: The Smart Irrigation Controller Rebate Program includes an emphasis on water use efficiency by different end users including residents, commercial, and other large irrigators. This requires the installation of irrigation equipment, specifically water efficient, weather-based smart controllers. These controllers will help maintain the landscape by automatically adjusting irrigation settings based on local weather conditions.

Mission Springs Water District (MSWD) Demonstration Garden: The demonstration garden will display water efficient irrigation systems, various ground covers, provide examples of maintaining challenging slopes and microclimates, as well as encourage the selection of current desert friendly varieties of plant material reflecting the most recent edition of the local MSWD's *Water Efficient Landscaping Guidelines* and *Water-Wise Plant Guide*. The centrally located garden will provide an excellent educational space for self-guided and group tours. The gardens will provide an area for educational workshops to provide real time demonstrations of topics such as pruning, vegetable gardening, selecting desert plants, and irrigation zones. The incorporation of technology is proposed into the garden via a web/phone application interface that will allow visitors to be able to look up in real time plant species, rock types, and irrigation elements by simply downloading the application and scanning an identification marker. Information will also be available in Spanish. The demonstration garden will educate the public on efficient outdoor water use, and visitors can apply efficient garden design in their own yards, thereby reducing water demands.

Indio Water Authority (IWA) Coachella Valley History Museum Gardens & Railway Project: The Coachella Valley History Museum has partnered with the Indio Water Authority for the Water Efficient Landscapes and Demonstration Garden and Railway Project. This Project will encompass a 15,000 square foot area in the northeast corner of the Coachella Valley History Museum campus that will feature an array of drought-tolerant desert gardens. IWA is committed to efficient water use through water-efficiency standards, practices, and incentives. The Garden Master Plan consists of 12 different gardens/lawns addressing different landscape needs. The Garden layout is designed to provide leadership through example and support IWA's existing landscape programs such as smart irrigation controllers and turf rebates. When completed, the Garden will become a community asset and learning center in Downtown Indio. Additionally, there will be signage that complies with State requirements and flyers about the project. It will also provide a central location for IWA staff to conduct public outreaches and encourage customers to adopt one of the many landscapes/gardens for their property.

Regional Conservation Study Project: The study component of the project, the Regional Conservation Study Project, is a decision-support tool (DST) that will guide the agencies as they work to determine incentive amounts and water supply benefits. The regional water outreach campaign, CV Water Counts, will promote the incentives and the study findings. The tool will: Quantify grass replacement program water

savings that account for local conditions and practices (local evapotranspiration (ET), soil types, irrigation efficiency); Quantify the cost per acre-foot for turf replacement and the return on investment for agencies and program participants; Develop data on the rate at which turf replacement participants return to turf after installing a low-water-use landscape; Quantify the amount of turf remaining in the Coachella Valley available for future conversions; Explore technologies that could better assist in monitoring of the items above; and Consider other variables that may inform water conservation program development.

Budget Category (a): Project Administration

Task 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/Easement

Task 3: Land Purchase

No land purchase or easement acquisition is required for this project.

Deliverables: N/A

Budget Category (c): Planning/Design/Engineering/Environmental Documentation

Task 4: Feasibility Studies

Not applicable to the project. No feasibility studies were completed as part of the project development process. The feasibility of the project is evident due to the many successful years of grass conversions.

Deliverables: N/A

Task 5: CEQA Documentation

The demonstration gardens fall under the CEQA exemption for Class 4: Minor Alterations to Land (CEQA 15304). A Notice of Exemption (NOE) is to be filed for the MSWD's Demonstration Garden and IWA's Coachella Valley History Museum Gardens and Railway Project. Prepare letter stating no legal challenges (or addressing legal challenges).

Deliverables:

- All completed CEQA documents as required
- Legal Challenges Letter

Task 6: Permitting

The MSWD's demonstration garden will require a building permit with the City of Desert Hot Springs. The Coachella Valley History Museum Gardens and Railway Project will require a grading permit. No other permits are required.

Deliverables:

- Permits as required

Task 7: Design

Design for the MSWD demonstration garden includes a topographical survey and irrigation plans. MSWD will hire a consultant to prepare a base map, plans and specifications for the demonstration garden. The design will include a grading and irrigation plan and will be prepared in coordination with the City of Desert Hot Springs.

Design for the Coachella Valley History Museum Gardens and Railway Project include a topographical survey, irrigation, planting and lighting plans, landscape plans, precise grading plan, and dust control plan.

Deliverables:

- MSWD Site Map
- IWA Site Map
- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/Implementation

Task 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents, prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed.

Deliverables:

- Bid Documents
- Proof of Advertisement
- Award of Contract
- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Construction

Construction and implementation activities are outlined below.

11(a): This task includes implementing the Regional Grass Replacement Program, including application review and approval, pre- and post-site visits to customer sites, verification of successful project completion, customer support, rebate check processing, and program website maintenance. This task also includes work to measure and report program progress and budgeted funds for materials and equipment necessary to implement the water-efficient landscape upgrades. Eligible costs include, but are not limited to: water-efficient plants, mulch, hardware (weather- based controllers, irrigation piping, meters, valves, etc.).

11(b): This subtask includes implementing the Smart Irrigation Controller Rebate Program, including application review and approval, pre-and post-site visits to customer sites, verification of successful project completion, customer support, rebate check processing, and program website maintenance. This task also includes work to measure and report program progress and budgeted funds for materials and equipment necessary to implement the water-efficient landscape upgrades. Eligible costs include, but are not limited to: water-efficient plants, mulch, hardware (weather- based controllers, irrigation piping, meters, valves, etc.).

11(c): MSWD Demonstration Garden Construction - This subtask includes construction of one garden. MSWD's Demonstration Garden will include site grading and soil preparation, installation of irrigation equipment, planting of desert-friendly plants, and application of fertilizer and mulch to protect new growth. The demonstration garden will be constructed to be aesthetically pleasing and will be included in the tour of the new Critical Services Center in Desert Hot Springs, allowing many visitors to observe it.

11(d): Regional Conservation Study Project – This subtask includes work to complete a study/decision support tool. The tool will guide the agencies as they work to determine incentive amounts and water supply benefits.

11(e): IWA Demonstration Garden Construction - This subtask includes construction of one garden consisting of 12 different gardens/lawns. The Demonstration Garden will include site grading and soil preparation, installation of irrigation equipment, and planting of a variety of vegetation compatible to the desert. The demonstration garden will showcase the beauty of drought-tolerant landscaping in a variety of garden themed landscapes.

Deliverables:

- Photographic Documentation of Progress
- Site visit reports (pre and post) to measure water use and confirm installations, if applicable
- Original customer receipts for all materials involved in the program, if applicable
- Maps with geographic locations of program participants, if applicable
- Report documenting compliance with water budgets, if applicable
- Regional Conservation Study Project Decision Support Tool

PROJECT 3: Groundwater Quality Protection Project – Area D-3**IMPLEMENTING AGENCY:** Mission Springs Water District (MSWD)**PROJECT DESCRIPTION:**

The project will construct Area D-3 to connect approximately 99 parcels to the MSWD sewer collection and treatment system and abate 79 on-site septic disposal systems, which includes a sewer mainline, sewer laterals, manholes, and associated improvements. The project will treat and recharge approximately 22.5 acre-feet per year (AFY) of wastewater into the local aquifer for the City of Desert Hot Springs and the Coachella Valley. This project will also have a nitrogen load reduction of 5.93lbs/day or 2,64 pounds of nitrogen per year. Over the 50-year life of this project, approximately 1,109 AF of wastewater will be collected, treated and recharged with significantly better water quality in this DAC.

Budget Category (a): Project AdministrationTask 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/EasementTask 3: Land Purchase

No land purchase or easement acquisition is required for this project as all work will be completed within the public right-of-way.

Deliverables: N/A**Budget Category (c): Planning/Design/Engineering/Environmental Documentation**Task 4: Feasibility Studies

Project Feasibility Studies were completed as part of the project development process. The following feasibility studies were completed as part of the project development process: 1996 Groundwater Flow Study

by Michigan Technological University; 1996 Groundwater Contamination Study by USGS; 2011 Nitrate Investigation in Groundwater by GSI Water; and 2019 Assessment District No. 18 Engineer's Report

Deliverables:

- Relevant Feasibility Studies

Task 5: CEQA Documentation

A Mitigated Negative Declaration was filed for this project with the State Clearinghouse in March 1999. An addendum was filed in March 2011. An additional addendum will be completed. Prepare letter stating no legal challenges (or addressing legal challenges).

Deliverables:

- All completed CEQA documents as required
- Legal Challenges Letter

Task 6: Permitting

The following permits will be acquired for this project: Encroachment permit from the City of Desert Hot Springs.

Deliverables:

- Permits as required

Task 7: Design

Design was completed in March 2015. Additional design refinements for this sub-area to commence once agreement is executed

Deliverables:

- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/Implementation

Task 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents, prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed.

Deliverables:

- Bid Documents
- Proof of Advertisement
- Award of Contract
- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives. A full-time engineering construction observer will be on site for the duration of the project. Construction observer duties include documenting of pre-construction conditions, daily construction diary, preparing change orders, addressing questions of contractors on site, reviewing/ updating project schedule, reviewing contractor log submittals and pay requests, forecasting cash flow, notifying contractor if work is not acceptable. Upon completing the project, the DWR Certificate of Project Completion and record drawings will be provided to DWR.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Construction

Construction activities are outlined below.

11(a): Mobilization includes equipment delivery, Stormwater Pollution Prevention Plan Best Management Practices installation and management, potholing, and traffic control. Demobilization includes removal of surplus materials and equipment from the project site.

11(b): Installation of approximately 4,720 linear feet of sewer mainline, 3,350 linear feet of 4-inch sewer laterals, 16 manholes, 20,000-square feet of pavement/trench repair, and associated improvements. This task also includes pavement removal, trenching, shoring, bedding, pipe installation, manhole installation, lateral construction, backfilling, compaction, connections, pavement restoration, striping, and clean up. Performance testing shall be per MSWD Developer/Contractors Guidelines Handbook and per the project plans and specifications. Inspection and testing are required by the project specifications. Testing includes air pressure testing of the sewer lines and backfill compaction testing. Return construction and staging areas as reasonably as possible to original or improved conditions as a result of construction activities, including newly paved streets.

Deliverables:

- Photographic Documentation of Progress
- Engineers Certification
- Performance Testing Results

PROJECT 4: Coachella Water Authority Groundwater Well Project**IMPLEMENTING AGENCY:** Coachella Water Authority (CWA)**PROJECT DESCRIPTION:**

The project will construct a groundwater well to provide the Coachella Valley with an additional 2,500 acre-feet per year (AFY) of water supply needed to serve three newly consolidated small water systems. The project will increase CWA's overall capacity, improve operational flexibility needed to meet demands, and improve water supply reliability for 45,522 customers served by CWA.

Budget Category (a): Project AdministrationTask 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/EasementTask 3: Land Purchase

No land purchase or easement acquisition is required for this project. The groundwater well will be located at one of two CWA-owned sites to be determined during preliminary design.

Deliverables: N/A**Budget Category (c): Planning/Design/Engineering/Environmental Documentation**Task 4: Feasibility Studies

Project Feasibility Studies were completed as part of the project development process. Preparation of a Well Siting Evaluation was completed in May 2017. No additional feasibility studies are required for this project.

Deliverables:

- Relevant Feasibility Studies

Task 5: CEQA Documentation

Complete environmental review pursuant to CEQA. Prepare all necessary environmental documentation. Prepare letter stating no legal challenges (or addressing legal challenges).

Deliverables:

- All completed CEQA documents as required
- Legal Challenges Letter

Task 6: Permitting

The permits will be identified during the design process. CWA will acquire all necessary permits prior to the start of construction and operation.

The following permits are anticipated to be acquired for this project: Permit to Construct, SCAQMD; Fugitive Dust Control Plan, SCQAMD; General Permit for Stormwater Discharge, SWRCB; General Permit for Construction Discharges, RWQCB.

Deliverables:

- Permits as required

Task 7: Design

Planning for the Project began in January 2017 with the preparation of a Well Siting Evaluation (see Task 4). Design for the Project is expected to begin upon receipt of State grant funding. CWA will hire a consultant to prepare 30%, 60%, 90% and Final plans and specifications for the project. During the preliminary design phase, CWA and its consultant will select the site based on the Well Siting Evaluation previously completed.

Deliverables:

- Basis of Design Report
- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/Implementation

Task 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents, prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed.

Deliverables:

- Bid Documents

- Proof of Advertisement
- Award of Contract
- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives. A full-time engineering construction observer will be on site for the duration of the project. Construction observer duties include documenting of pre-construction conditions, daily construction diary, preparing change orders, addressing questions of contractors on site, reviewing/ updating project schedule, reviewing contractor log submittals and pay requests, forecasting cash flow, notifying contractor if work is not acceptable. Upon completing the project, the DWR Certificate of Project Completion and record drawings will be provided to DWR.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Construction

Construction activities are outlined below.

11(a): Mobilization and demobilization activities, including: preparing, submitting, and responding to submittals; all contractor administrative requirements (e.g., bonds, insurance); site cleanup and site restoration (e.g., final grading, landscaping, touch-up paint); furnishing all documentation (warranties, manuals, Standard Operating Procedure); and removal of all temporary facilities.

11(b): Site preparation activities, including: setting up temporary facilities (e.g., field office, construction barriers).

11(c): Construction will consist of drilling, testing, casing, and developing an approximately 2,200- gallon per minute (gpm) groundwater well that will be approximately 1,300 feet deep with an approximately 18-inch diameter casing and screen. The exact depth and casing diameter will be determined during the design and implementation process. The Project will also construct the well manifold piping, pump house, electrical building, installation of the electrical motor control center, hydropneumatics tank, emergency backup generator, chlorination equipment, site grading, other related aboveground and underground appurtenances, and connection to CWA's existing domestic water distribution system.

Deliverables:

- Photographic Documentation of Progress
- Engineers Certification
- Performance Testing Results

PROJECT 5: Polanco Septic Rehabilitation Program

Amendment 2: Project 5 Removed and Replaced with Project 8

PROJECT 6: Sunrise Park Recycled Water Connection

IMPLEMENTING AGENCY: Desert Water Agency (DWA)

PROJECT DESCRIPTION:

The project will connect Sunrise Park, home to Mizell Senior Center and Boys & Girls Club of Palm Springs, to recycled water. The project includes the addition of a booster station, approximately 4,000 lineal feet of recycled water pipe and some onsite connection retrofits for 11 services. The capacity at the existing water recycling plant is sufficient to handle the additional demand so no upgrades are necessary at that facility as a result of this project. The project will provide 199 acre-feet per year (AFY) of recycled water, decreasing demand of groundwater pumping.

Budget Category (a): Project Administration

Task 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

DWA will coordinate with the City of Palm Springs regarding onsite plumbing retrofits and invoices, compile DWA invoices for material, contracts and labor related to construction and share materials with Coachella Valley Water District for DWR invoicing.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

DWA will coordinate with City of Palm Springs on progress for onsite plumbing retrofits, recycled water permit and coordinate with DWA project manager and contractors on project status and milestones.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/Easement

Task 3: Land Purchase

DWA will determine site requirements for the booster station. Identify possible parcels for purchase if DWA does not own an ideal site. Commission an appraisal, if necessary. Get Board of Directors approval for land purchase, if necessary. Complete escrow for land acquisition, if necessary.

Deliverables:

- Documentation supporting property value (if purchased)
- All relevant documentation regarding property ownership transfer or acquisition of easement including final recorded deed, title report, etc.

Budget Category (c): Planning/Design/Engineering/Environmental DocumentationTask 4: Feasibility Studies

Not applicable to the project. No feasibility studies were completed as part of the project development process.

Deliverables: N/A

Task 5: CEQA Documentation

Complete environmental review pursuant to CEQA. Prepare all necessary environmental documentation. Prepare letter stating no legal challenges (or addressing legal challenges).

Deliverables:

- All completed CEQA documents as required
- Legal Challenges Letter

Task 6: Permitting

The following permits are anticipated to be acquired for this project: 1) an encroachment/construction permit from the City of Palm Springs for construction in public right of way, and 2) a permit from the Regional Water Quality Control Board for use of recycled water at the site.

Deliverables:

- Permits as required

Task 7: Design

Complete engineering design for pipeline extension and booster station and plans for onsite retrofits. Prepare and complete 100% design drawings and specifications.

Deliverables:

- Basis of Design Report
- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/Implementation

Task 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents, prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed.

DWA will prepare bid documents for pipeline extension and booster station, advertise for submissions, review bids, take selected bid(s) to Board of Directors for approval. City of Palm Springs to prepare bid documents for necessary onsite plumbing retrofits, advertise for submissions, review bids, take selected bid(s) to City Council for approval.

Deliverables:

- Bid Documents
- Proof of Advertisement
- Award of Contract
- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives. A full-time engineering construction observer will be on site for the duration of the project. Construction observer duties include documenting of pre-construction conditions, daily construction diary, preparing change orders, addressing questions of contractors on site, reviewing/ updating project schedule, reviewing contractor log submittals and pay requests, forecasting cash flow, notifying contractor if work is not acceptable. Upon completing the project, the DWR Certificate of Project Completion and record drawings will be provided to DWR. DWA will oversee construction schedule, coordinate public notifications on project traffic and noise impacts, have an inspector onsite, manage contractor payments.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Construction

Construction activities are outlined below.

11(a): Mobilization and demobilization activities, including: preparing, submitting, and responding to submittals; all contractor administrative requirements (e.g., bonds, insurance); site cleanup and site restoration (e.g., final grading, landscaping, touch-up paint); furnishing all documentation (warranties, manuals, Standard Operating Procedure); and removal of all temporary facilities.

11(b): Site preparation activities, including: setting up temporary facilities (e.g., field office, construction barriers).

11(c): Construction activities include the construction of roughly 4,000 lineal feet of pipeline, retrofit existing onsite plumbing to prepare for transition to recycled water, eliminate mixed-use meters, and build and connect booster station.

Deliverables:

- Photographic Documentation of Progress
- Engineers Certification
- Performance Testing Results

PROJECT 7: Stannous Chloride Demonstration Project**IMPLEMENTING AGENCY:** Coachella Valley Water District (CVWD)

PROJECT DESCRIPTION: The project will construct a pipe rig and implement testing of Stannous Chloride treatment without filtration to reduce hexavalent Chromium (Chromium-6) to trivalent chromium (Chromium-3), which is significantly less toxic than Chromium-6, for one well in the Improvement District No. 8 (ID-8) Public Water System. The project will reduce Chromium-6 to levels to <8 ug/L, which is below the State Water Board threshold of 10 µg/L. The reduction will allow the ID-8 public water system to continue production, which averages 2,903 AFY. It will also ensure water supply reliability to 4,600 people in the ID-8 public water system, which qualifies as severely disadvantaged community and disadvantaged community. Results from this project will determine whether Stannous Chloride can be effectively used as a treatment option for all four wells in the ID-8 public water system that have high Chromium-6 levels and for all 35 of CVWD's impacted wells, benefiting over 270,000 customers. Additionally, CVWD will make results from this project available to all agencies in the Coachella Valley Regional Water Management Group as well as the Division of Drinking Water, and thus, agencies can use these results to determine if Stannous Chloride treatment without filtration is feasible for their public water system.

Budget Category (a): Project AdministrationTask 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/Easement

Task 3: Land Purchase

No land purchase or easement acquisition is required for this project.

Deliverables: N/A

Budget Category (c): Planning/Design/Engineering/Environmental Documentation

Task 4: Feasibility Studies

Demonstration Study has been completed. Testing plans will be completed as part of the project development process.

Deliverables:

- Relevant Testing Plans
- Demonstration Study

Task 5: CEQA Documentation

The project is not considered a project under CEQA as it will not have a direct or reasonably foreseeable indirect impact on the environment. The pipe rig will be housed within an existing building at an existing site well.

Deliverables: N/A

Task 6: Permitting

No permits are required for the project.

Deliverables: N/A

Task 7: Design

Complete design of the pipe rig, with 100% Design Plans and Specifications.

Deliverables:

- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/Implementation

Task 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents,

prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed. Coordinate obtaining bids from general contractors and vendors. CVWD already completed all contract services and will submit all applicable documentation.

Deliverables:

- Bid Documents
- Proof of Advertisement
- Award of Contract
- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives. A full-time engineering construction observer will be on site for the duration of the project. Construction observer duties include documenting of pre-construction conditions, daily construction diary, preparing change orders, addressing questions of contractors on site, reviewing/ updating project schedule, reviewing contractor log submittals and pay requests, forecasting cash flow, notifying contractor if work is not acceptable. Upon completing the project, the DWR Certificate of Project Completion and record drawings will be provided to DWR.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Implementation

Implementation activities are outlined below.

11(a): Mobilization and demobilization activities, including: Oversee construction of the pipe rig. This includes site preparation, providing needed source water connections and valves, electrical power, and assisting with assembly.

11(b): Construction activities include the construction of roughly 4,000 lineal feet of pipeline, retrofit existing onsite plumbing to prepare for transition to recycled water, eliminate mixed-use meters, and build and connect booster station.

11(c): Evaluate several risks and uncertainties associated with Stannous Chloride treatment without filtration. Testing includes, but not limited to:

- Operations with new pipe materials: Pipe rig consisting of new pipe materials (copper, and polyvinyl chloride, with and without Stannous Chloride addition.
- Operations with harvested pipe materials: Pipe rig consisting of harvested pipe materials (copper, galvanized steel, and polyvinyl chloride), with and without Stannous Chloride addition.

Deliverables:

- Photographic Documentation of Progress
- Testing Results

PROJECT 8: Reservoir 7802-2 Project**IMPLEMENTING AGENCY:** Coachella Valley Water District (CVWD)

PROJECT DESCRIPTION: The Project will construct Reservoir 7802-2, a new 5 million gallon (MG) welded steel reservoir in the Middleton Pressure Zone, within the District. The Middleton Pressure Zone is impacted by arsenic and Chromium-6, posing public health concerns as exposure to both contaminants can lead to several health issues, such as cancer and cardiovascular disease. The Project will restore and improve water storage infrastructure by providing 5 MG of water storage to ensure reliable and sustainable domestic water supply and fire flow protection to CVWD's customers. The project will also improve water supply reliability for approximately 11,700 people living in the Middleton Pressure Zone, which is classified as a severely disadvantaged community.

Budget Category (a): Project AdministrationTask 1: Project Management

Manage Grant Agreement including compliance with grant requirements, and preparation and submission of supporting grant documents and coordination with IRWM regional manager. Prepare invoices including relevant supporting documentation for submittal to DWR via the Grantee. This task also includes administrative responsibilities associated with the project such as coordinating with partnering agencies and managing consultants/contractors.

Deliverables:

- Invoices and associated backup documentation

Task 2: Reporting

Prepare progress reports detailing work completed during reporting period as outlined in Exhibit F of this Agreement. Submit reports to DWR.

Prepare Project Completion Report and submit to DWR no later than 90 days after project completion for DWR Project Manager's comment and review. The report shall be prepared and presented in accordance with guidance as outlined in Exhibit F.

Deliverables:

- Quarterly Project Progress Reports
- Project Completion Report
- Documentation (e.g., photo) of "Acknowledgment of Credit & Signage" per Standard Condition D.2

Budget Category (b): Land Purchase/EasementTask 3: Land Purchase

No land purchase or easement acquisition is required for this project.

Deliverables: N/A

Budget Category (c): Planning/Design/Engineering/Environmental DocumentationTask 4: Feasibility Studies

Not applicable to the project.

Deliverables: N/A

Task 5: CEQA Documentation

Environmental documents are in the final stages of completion. An environmental impact report is being prepared for the project area. The environmental impact report will include construction of the reservoir. anticipated completion date of the environmental documentation is January 2025. CVWD will prepare a letter stating no legal challenges.

Deliverables:

- All completed CEQA documents as required
- Legal Challenges Letter

Task 6: Permitting

Not applicable. There are no permits required for this project.

Deliverables:

- N/A

Task 7: Design

Design is 100% complete.

Deliverables:

- 100% Design Plans and Specifications

Task 8: Project Monitoring Plan

Develop and submit a Project Monitoring Plan per Paragraph 16 for DWR's review and approval.

Deliverables:

- Project Monitoring Plan

Budget Category (d): Construction/ImplementationTask 9: Contract Services

This task must comply with the Standard Condition D.11 – Competitive Bidding and Procurements. Activities necessary (as applicable) to secure a contractor and award the contract, including: develop bid documents, prepare advertisement and contract documents for construction contract bidding, conduct pre-bid meeting, bid opening and evaluation, selection of the contractor, award of contract, and issuance of notice to proceed.

Deliverables:

- Bid Documents
- Proof of Advertisement
- Award of Contract

- Notice to Proceed

Task 10: Construction Administration

This task includes managing contractor submittal review, answering requests for information, and issuing work directives. A full-time engineering construction observer will be on site for the duration of the project. Construction observer duties include documenting of pre-construction conditions, daily construction diary, preparing change orders, addressing questions of contractors on site, reviewing/ updating project schedule, reviewing contractor log submittals and pay requests, forecasting cash flow, notifying contractor if work is not acceptable. Upon completing the project, the DWR Certificate of Project Completion and record drawings will be provided to DWR.

Deliverables:

- DWR Certificate of Project Completion
- Record Drawings
- Inspection Reports

Task 11: Construction

Construction activities are outlined below.

11(a): Mobilization and demobilization activities, including: preparing, submitting, and responding to submittals; all contractor administrative requirements (e.g., bonds, insurance); site cleanup and site restoration (e.g., final grading, landscaping, touch-up paint); furnishing all documentation (warranties, manuals, Standard Operating Procedure); and removal of all temporary facilities.

11(b): Site preparation activities, including: setting up temporary facilities (e.g., field office, construction barriers).

11(c): Construction activities include earthwork and site work including excavating, importing, exporting, trenching, scarifying, backfilling, placing, filling, compacting, and grading all soil and rock materials onsite; furnishing and installing site piping and all related work; leakage and pressure testing pipelines; furnishing and installing all electrical service equipment, electrical panels, instrumentation and controls, lighting, conduit, and conductors; furnishing and erecting one (1) new 5.0 MG welded steel potable water storage reservoir with appurtenances; and constructing reinforcing concrete ringwall and related asphalt sand and clean sand foundation beneath reservoir.

Deliverables:

- Photographic Documentation of Progress
- Test results

EXHIBIT B
BUDGET

PROPOSITION 1 ROUND 2 COACHELLA VALLEY IRWM IMPLEMENTATION GRANT

AGREEMENT BUDGET SUMMARY

	PROJECTS	Grant Amount	Required Cost Share: Non-State Fund Source	Other Cost Share	Total Cost	Required Cost Share %
	Grant Administration	\$25,000	\$0	\$0	\$25,000	N/A
1*	Project 1: Reservoirs 4711-3 and 4711-4 Construction Project*					
2	Project 2: Desert Water Agency Regional Conservation Program	\$812,755	\$812,755	\$0	\$1,625,510	50%
3	Project 3: Groundwater Quality Protection Project – Area D-3	\$875,000	\$875,000	\$245,000	\$1,995,000	50%
4	Project 4: Coachella Water Authority Groundwater Well Project	\$750,000	\$0	\$3,145,291	\$3,895,291	0%
5**	Project 5: Polanco Septic Rehabilitation Project**					
6	Project 6: Sunrise Park Recycled Water Connection	\$500,000	\$520,500	\$20,500	\$1,041,000	50%
7	Project 7: Stannous Chloride Demonstration Testing	\$300,000	\$0	\$846,978	\$1,146,978	0%
9	Project 8: Reservoir 7802-2	\$850,000	\$0	\$5,150,000	\$6,000,000	0%
	GRAND TOTAL	\$4,112,755	\$2,208,255	\$9,407,769	\$15,728,779	

Notes:

*Project 1 removed and replaced by Project 7 in Amendment 2.

**Project 5 removed and replaced with Project 8 in Amendment 2.

Grant Administration

Implementing Agency: Coachella Valley Water District (CVWD)

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source	Other Cost Share	Total Cost
(a)	Project Administration	\$25,000	\$0	\$0	\$25,000
	TOTAL COSTS	\$25,000	\$0	\$0	\$25,000

PROJECT 1: Reservoirs 4711-3 and 4711-4 Construction Project

Amendment 2: Project 1 Removed and Replaced by Project 7

PROJECT 2: Desert Water Agency Regional Conservation Program

Implementing Agency: Desert Water Agency

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share	Total Cost
(a)	Project Administration	\$0	\$0	\$0	\$0
(b)	Land Purchase / Easement	\$0	\$0	\$0	\$0
(c)	Planning / Design / Engineering / Environmental Documentation	\$0	\$0	\$0	\$0
(d)	Construction / Implementation	\$812,755	\$812,755	\$0	\$1,625,510
	TOTAL COSTS	\$812,755	\$812,755	\$0	\$1,625,510

NOTES:

Eligible costs for each Budget Category will only be approved for reimbursement and Cost Share for the work completed within the date ranges listed in Exhibit C.

* Required Cost Share fund source(s): Coachella Valley Water District, Indio Water Authority and Mission Springs Water District budgets.

PROJECT 3: Groundwater Quality Protection Project – Area D-3

Implementing Agency: Mission Springs Water District

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share**	Total Cost
(a)	Project Administration	\$0	\$0	\$12,000	\$12,000
(b)	Land Purchase / Easement	\$0	\$0	\$0	\$0
(c)	Planning / Design / Engineering / Environmental Documentation	\$0	\$0	\$39,500	\$39,500
(d)	Construction / Implementation	\$875,000	\$875,000	\$193,500	\$1,943,500
TOTAL COSTS		\$875,000	\$875,000	\$245,000	\$1,995,000

NOTES:

Eligible costs for each Budget Category will only be approved for reimbursement and Cost Share for the work completed within the date ranges listed in Exhibit C.

* Required Cost Share fund source(s): Assessment District 18 proceeds.

** Other Cost Share fund source(s): Local assessment district and sewer improvement funds.

PROJECT 4: Coachella Water Authority Groundwater Well Project

Implementing Agency: Coachella Water Authority

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share**	Total Cost
(a)	Project Administration	\$0	\$0	\$40,000	\$40,000
(b)	Land Purchase / Easement	\$0	\$0	\$0	\$0
(c)	Planning / Design / Engineering / Environmental Documentation	\$0	\$0	\$100,000	\$100,000
(d)	Construction / Implementation	\$750,000	\$0	\$3,005,291	\$3,755,291
TOTAL COSTS		\$750,000	\$0	\$3,145,291	\$3,895,291

NOTES:

Eligible costs for each Budget Category will only be approved for reimbursement and Cost Share for the work completed within the date ranges listed in Exhibit C.

*The project received a 100% cost share waiver.

**Other Cost Share fund source(s): Coachella Water Agency General Fund

PROJECT 5: Polanco Septic Rehabilitation Program

Amendment 2: Project 5 Removed and Replaced by Project 8

PROJECT 6: Sunrise Park Recycled Water Connection

Implementing Agency: Desert Water Agency (DWA)

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share**	Total Cost
(a)	Project Administration	\$0	\$30,000	\$0	\$30,000
(b)	Land Purchase / Easement	\$0	\$0	\$0	\$0
(c)	Planning / Design / Engineering / Environmental Documentation	\$0	\$67,500	\$6,000	\$73,500
(d)	Construction / Implementation	\$500,000	\$423,000	\$14,500	\$937,500
	TOTAL COSTS	\$500,000	\$520,500	\$20,500	\$1,041,000

NOTES:

Eligible costs for each Budget Category will only be approved for reimbursement and Cost Share for the work completed within the date ranges listed in Exhibit C.

*Required Cost Share fund source(s): DWA and City of Palm Springs funds, possible federal funding.

**Other Cost Share fund source(s): DWA Capital Improvement Budget

PROJECT 7: Stannous Chloride Demonstration Testing

Implementing Agency: Coachella Valley Water District (CVWD)

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share**	Total Cost
(a)	Project Administration	\$0	\$0	\$109,749	\$109,749
(b)	Land Purchase/Easement	\$0	\$0	\$0	\$0
(c)	Planning/Design/Engineering/Environmental	\$0	\$0	\$0	\$0
(d)	Construction/Implementation	\$300,000	\$0	\$737,229	\$1,037,229
		\$300,000	\$0	\$846,978	\$1,146,978

NOTES:

Eligible costs for each Budget Category will only be approved for reimbursement and Cost Share for the work completed within the date ranges listed in Exhibit C.

*The project received a 100% cost share waiver.

** Other Cost Share fund source(s): CVWD Domestic Fund

PROJECT 8: Reservoir 7802-2

Implementing Agency: Coachella Valley Water District

	BUDGET CATEGORY	Grant Amount	Required Cost Share: Non-State Fund Source*	Other Cost Share	Total Cost
(a)	Project Administration	\$0	\$0	\$35,000	\$35,000
(b)	Land Purchase/Easement	\$0	\$0	\$0	\$0
(c)	Planning/Design/Engineering/Environmental	\$0	\$0	\$0	\$0
(d)	Construction/Implementation	\$850,000	\$0	\$5,150,000	\$6,000,000
		\$850,000	\$0	\$5,185,000	\$6,035,000

NOTES:

*The project received a 100% cost share waiver.

** Other Cost Share fund source(s): CVWD Water System Backup Facilities Charge Fund and Thermal Ranch, LLC

**EXHIBIT C
SCHEDULE**

PROPOSITION 1 ROUND 2 COACHELLA VALLEY IRWM IMPLEMENTATION GRANT

Grant Administration

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	01/31/2023	03/31/2027

PROJECT 1: Reservoirs 4711-3 and 4711-4 Construction Project

Amendment 2: Project 1 Removed and Replaced by Project 7

PROJECT 2: Desert Water Agency Regional Conservation Program

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	01/31/2023	09/30/2026
b	Land Purchase / Easement	N/A	N/A
c	Planning / Design / Engineering / Environmental Documentation	01/31/2023	09/30/2023
d	Construction / Implementation	07/01/2022	07/31/2026

The schedules for categories c and d will overlap because implementation of grass removal and study will begin immediately prior to completion of the planning/design/permitting for the Demonstration Garden.

PROJECT 3: Groundwater Quality Protection Project – Area D-3

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	01/31/2023	12/31/2026
b	Land Purchase / Easement	N/A	N/A
c	Planning / Design / Engineering / Environmental Documentation	04/01/2023	03/31/2024
d	Construction / Implementation	04/01/2024	09/30/2026

PROJECT 4: Coachella Water Authority Groundwater Well Project

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	08/14/2024	12/31/2026
b	Land Purchase / Easement	N/A	N/A
c	Planning / Design / Engineering / Environmental Documentation	07/01/2024	06/30/2025
d	Construction / Implementation	07/01/2025	09/30/2026

PROJECT 5: Polanco Septic Rehabilitation Program

Amendment 2: Project 5 Removed and Replaced by Project 8

PROJECT 6: Sunrise Park Recycled Water Connection

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	01/31/2023	10/31/2026
b	Land Purchase / Easement	02/01/2023	12/31/2024
c	Planning / Design / Engineering / Environmental Documentation	01/31/2023	06/30/2025
d	Construction / Implementation	07/01/2025	07/30/2026

PROJECT 7 Stannous Chloride Demonstration Testing

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	8/20/2024	03/31/2026
b	Land Purchase / Easement	N/A	N/A
c	Planning / Design / Engineering / Environmental Documentation	8/20/2024	10/31/2024
d	Construction / Implementation	9/30/2024	12/31/2025

Note: There is overlap between Category C and Category D to allow for some design adjustments during construction.

PROJECT 8 Reservoir 7802-2

	BUDGET CATEGORY	Start Date	End Date
a	Project Administration	02/01/2024	12/31/2026
b	Land Purchase / Easement	N/A	N/A
c	Planning / Design / Engineering / Environmental Documentation	02/01/2024	02/14/2025
d	Construction / Implementation	09/30/2025	09/30/2026

Note: The schedule is dependent on the Developer's timing. The Developer intends to bid the project in Quarter 3 of 2025 or possibly as late as Quarter 4 of 2025.

EXHIBIT D**STANDARD CONDITIONS**

- D.1. **ACCOUNTING AND DEPOSIT OF FUNDING DISBURSEMENT:**
- A. **Separate Accounting of Funding Disbursements:** Grantee shall account for the money disbursed pursuant to this Grant Agreement separately from all other Grantee funds. Grantee shall maintain audit and accounting procedures that are in accordance with generally accepted accounting principles and practices, consistently applied. Grantee shall keep complete and accurate records of all receipts and disbursements on expenditures of such funds. Grantee shall require its contractors or subcontractors to maintain books, records, and other documents pertinent to their work in accordance with generally accepted accounting principles and practices. Records are subject to inspection by State at any and all reasonable times.
 - B. **Disposition of Money Disbursed:** All money disbursed pursuant to this Grant Agreement shall be deposited in a non-interest bearing account, administered, and accounted for pursuant to the provisions of applicable law.
 - C. **Remittance of Unexpended Funds:** Grantee shall remit to State any unexpended funds that were disbursed to Grantee under this Grant Agreement and were not used to pay Eligible Project Costs within a period of sixty (60) calendar days from the final disbursement from State to Grantee of funds or, within thirty (30) calendar days of the expiration of the Grant Agreement, whichever comes first.
- D.2. **ACKNOWLEDGEMENT OF CREDIT AND SIGNAGE:** Grantee shall include appropriate acknowledgement of credit to the State for its support when promoting the Project or using any data and/or information developed under this Grant Agreement. Signage shall be posted in a prominent location at Project site(s) (if applicable) or at the Grantee's headquarters and shall include the Department of Water Resources color logo and the following disclosure statement: "Funding for this project has been provided in full or in part from the Water Quality, Supply, and Infrastructure Improvement Act of 2014 and through an agreement with the State Department of Water Resources." The Grantee shall also include in each of its contracts for work under this Agreement a provision that incorporates the requirements stated within this Paragraph.
- D.3. **AMENDMENT:** This Grant Agreement may be amended at any time by mutual agreement of the Parties, except insofar as any proposed amendments are in any way contrary to applicable law. Requests by the Grantee for amendments must be in writing stating the amendment request and the reason for the request. Requests solely for a time extension must be submitted at least 90 days prior to the work completion date set forth in Paragraph 2. Any other request for an amendment must be submitted at least 180 days prior to the work completion date set forth in Paragraph 2. State shall have no obligation to agree to an amendment.
- D.4. **AMERICANS WITH DISABILITIES ACT:** By signing this Grant Agreement, Grantee assures State that it complies with the Americans with Disabilities Act (ADA) of 1990, (42 U.S.C. § 12101 et seq.), which prohibits discrimination on the basis of disability, as well as all applicable regulations and guidelines issued pursuant to the ADA.
- D.5. **AUDITS:** State reserves the right to conduct an audit at any time between the execution of this Grant Agreement and the completion of the Project, with the costs of such audit borne by State. After completion of the Project, State may require Grantee to conduct a final audit to State's specifications, at Grantee's expense, such audit to be conducted by and a report prepared by an independent Certified Public Accountant. Failure or refusal by Grantee to comply with this provision shall be considered a breach of this Grant Agreement, and State may elect to pursue any remedies provided in Paragraph 12 or take any other action it deems necessary to protect its interests. The Grantee agrees it shall return any audit disallowances to the State.

Pursuant to Government Code section 8546.7, the Grantee shall be subject to the examination and audit by the State for a period of three (3) years after final payment under this Grant Agreement with respect of all matters connected with this Grant Agreement, including but not limited to, the cost of administering this Grant Agreement. All records of Grantee or its contractor or subcontractors shall be preserved for this purpose for at least three (3) years after receipt of the final disbursement under this Agreement. If an audit reveals any impropriety, the Bureau of State Audits or the State Controller's Office may conduct a full audit of any or all of the Grantee's activities. Code, § 79708, subd. (b)

- D.6. **BUDGET CONTINGENCY:** If the Budget Act of the current year covered under this Grant Agreement does not appropriate sufficient funds for this program, this Grant Agreement shall be of no force and effect. This provision shall be construed as a condition precedent to the obligation of State to make any payments under this Grant Agreement. In this event, State shall have no liability to pay any funds whatsoever to Grantee or to furnish any other considerations under this Grant Agreement and Grantee shall not be obligated to perform any provisions of this Grant Agreement. Nothing in this Grant Agreement shall be construed to provide Grantee with a right of priority for payment over any other Grantee. If funding for any fiscal year after the current year covered by this Grant Agreement is reduced or deleted by the Budget Act, by Executive Order, or by order of the Department of Finance, the State shall have the option to either cancel this Grant Agreement with no liability occurring to State, or offer a Grant Agreement amendment to Grantee to reflect the reduced amount.
- D.7. **CALIFORNIA CONSERVATION CORPS:** Grantee may use the services of the California Conservation Corps or other community conservation corps as defined in Public Resources Code section 14507.5.
- D.8. **CEQA:** Activities funded under this Grant Agreement, regardless of funding source, must be in compliance with the California Environmental Quality Act (CEQA). (Pub. Resources Code, § 21000 et seq.) Any work that is subject to CEQA and funded under this Agreement shall not proceed until documents that satisfy the CEQA process are received by the State's Project Manager and the State has completed its CEQA compliance. Work funded under this Agreement that is subject to a CEQA document shall not proceed until and unless approved by the Department of Water Resources. Such approval is fully discretionary and shall constitute a condition precedent to any work for which it is required. If CEQA compliance by the Grantee is not complete at the time the State signs this Agreement, once State has considered the environmental documents, it may decide to require changes, alterations, or other mitigation to the Project; or to not fund the Project. Should the State decide to not fund the Project, this Agreement shall be terminated in accordance with Paragraph 12, "Default Provisions."
- D.9. **CHILD SUPPORT COMPLIANCE ACT:** The Grantee acknowledges in accordance with Public Contract Code section 7110, that:
- A. The Grantee recognizes the importance of child and family support obligations and shall fully comply with all applicable state and federal laws relating to child and family support enforcement, including, but not limited to, disclosure of information and compliance with earnings assignment orders, as provided in Family Code section 5200 et seq.; and
 - B. The Grantee, to the best of its knowledge is fully complying with the earnings assignment orders of all employees and is providing the names of all new employees to the New Hire Registry maintained by the California Employment Development Department.
- D.10. **CLAIMS DISPUTE:** Any claim that the Grantee may have regarding performance of this Agreement including, but not limited to, claims for additional compensation or extension of time, shall be submitted to the DWR Project Representative, within thirty (30) days of the Grantee's knowledge of the claim. State and Grantee shall then attempt to negotiate a resolution of such claim and process an amendment to this Agreement to implement the terms of any such resolution.

- D.11. **COMPETITIVE BIDDING AND PROCUREMENTS:** Grantee's contracts with other entities for the acquisition of goods and services and construction of public works with funds provided by State under this Grant Agreement must be in writing and shall comply with all applicable laws and regulations regarding the securing of competitive bids and undertaking competitive negotiations. If the Grantee does not have a written policy to award contracts through a competitive bidding or sole source process, the Department of General Services' *State Contracting Manual* rules must be followed and are available at: <https://www.dgs.ca.gov/OLS/Resources/Page-Content/Office-of-Legal-Services-Resources-List-Folder/State-Contracting>.
- D.12. **COMPUTER SOFTWARE:** Grantee certifies that it has appropriate systems and controls in place to ensure that state funds will not be used in the performance of this Grant Agreement for the acquisition, operation, or maintenance of computer software in violation of copyright laws.
- D.13. **CONFLICT OF INTEREST:** All participants are subject to State and Federal conflict of interest laws. Failure to comply with these laws, including business and financial disclosure provisions, will result in the application being rejected and any subsequent contract being declared void. Other legal action may also be taken. Applicable statutes include, but are not limited to, Government Code section 1090 and Public Contract Code sections 10410 and 10411, for State conflict of interest requirements.
- A. **Current State Employees:** No State officer or employee shall engage in any employment, activity, or enterprise from which the officer or employee receives compensation or has a financial interest and which is sponsored or funded by any State agency, unless the employment, activity, or enterprise is required as a condition of regular State employment. No State officer or employee shall contract on his or her own behalf as an independent contractor with any State agency to provide goods or services.
- B. **Former State Employees:** For the two-year period from the date he or she left State employment, no former State officer or employee may enter into a contract in which he or she engaged in any of the negotiations, transactions, planning, arrangements, or any part of the decision-making process relevant to the contract while employed in any capacity by any State agency. For the twelve-month period from the date he or she left State employment, no former State officer or employee may enter into a contract with any State agency if he or she was employed by that State agency in a policy-making position in the same general subject area as the proposed contract within the twelve-month period prior to his or her leaving State service.
- C. **Employees of the Grantee:** Employees of the Grantee shall comply with all applicable provisions of law pertaining to conflicts of interest, including but not limited to any applicable conflict of interest provisions of the California Political Reform Act. (Gov. Code, § 87100 et seq.)
- D. **Employees and Consultants to the Grantee:** Individuals working on behalf of a Grantee may be required by the Department to file a Statement of Economic Interests (Fair Political Practices Commission Form 700) if it is determined that an individual is a consultant for Political Reform Act purposes.
- D.14. **DELIVERY OF INFORMATION, REPORTS, AND DATA:** Grantee agrees to expeditiously provide throughout the term of this Grant Agreement, such reports, data, information, and certifications as may be reasonably required by State.
- D.15. **DISPOSITION OF EQUIPMENT:** Grantee shall provide to State, not less than thirty (30) calendar days prior to submission of the final invoice, an itemized inventory of equipment purchased with funds provided by State. The inventory shall include all items with a current estimated fair market value of more than \$5,000.00 per item. Within sixty (60) calendar days of receipt of such inventory State shall provide Grantee with a list of the items on the inventory that State will take title to. All other items shall become the property of Grantee. State shall arrange for delivery from Grantee of items that it takes title to. Cost of transportation, if any, shall be borne by State.

- D.16. **DRUG-FREE WORKPLACE CERTIFICATION:** Certification of Compliance: By signing this Grant Agreement, Grantee, its contractors or subcontractors hereby certify, under penalty of perjury under the laws of State of California, compliance with the requirements of the Drug-Free Workplace Act of 1990 (Gov. Code, § 8350 et seq.) and have or will provide a drug-free workplace by taking the following actions:
- A. Publish a statement notifying employees, contractors, and subcontractors that unlawful manufacture, distribution, dispensation, possession, or use of a controlled substance is prohibited and specifying actions to be taken against employees, contractors, or subcontractors for violations, as required by Government Code section 8355.
 - B. Establish a Drug-Free Awareness Program, as required by Government Code section 8355 to inform employees, contractors, or subcontractors about all of the following:
 - i. The dangers of drug abuse in the workplace,
 - ii. Grantee's policy of maintaining a drug-free workplace,
 - iii. Any available counseling, rehabilitation, and employee assistance programs, and
 - iv. Penalties that may be imposed upon employees, contractors, and subcontractors for drug abuse violations.
 - C. Provide, as required by Government Code section 8355, that every employee, contractor, and/or subcontractor who works under this Grant Agreement:
 - i. Will receive a copy of Grantee's drug-free policy statement, and
 - ii. Will agree to abide by terms of Grantee's condition of employment, contract or subcontract.
- D.17. **EASEMENTS:** Where the Grantee acquires property in fee title or funds improvements to real property using State funds provided through this Grant Agreement, an appropriate easement or other title restriction providing for floodplain preservation and agricultural and/or wildlife habitat conservation for the subject property in perpetuity, approved by the State, shall be conveyed to a regulatory or trustee agency or conservation group acceptable to the State. The easement or other title restriction must be in first position ahead of any recorded mortgage or lien on the property unless this requirement is waived by the State.
- Where the Grantee acquires an easement under this Agreement, the Grantee agrees to monitor and enforce the terms of the easement, unless the easement is subsequently transferred to another land management or conservation organization or entity with State permission, at which time monitoring and enforcement responsibilities will transfer to the new easement owner.
- Failure to provide an easement or other title restriction acceptable to the State may result in termination of this Agreement.
- D.18. **FINAL INSPECTIONS AND CERTIFICATION OF REGISTERED PROFESSIONAL:** Upon completion of the Project, Grantee shall provide for a final inspection and certification by a California Registered Professional (i.e., Professional Civil Engineer, Engineering Geologist), that the Project has been completed in accordance with submitted final plans and specifications and any modifications thereto and in accordance with this Grant Agreement.
- D.19. **GRANTEE'S RESPONSIBILITIES:** Grantee and its representatives shall:
- A. Faithfully and expeditiously perform or cause to be performed all project work as described in Exhibit A and in accordance with Exhibits B and C.
 - B. Accept and agree to comply with all terms, provisions, conditions, and written commitments of this Grant Agreement, including all incorporated documents, and to fulfill all assurances, declarations, representations, and statements made by Grantee in the application, documents, amendments, and communications filed in support of its request for funding.
 - C. Comply with all applicable California, federal, and local laws and regulations.
 - D. Implement the Project in accordance with applicable provisions of the law.
 - E. Fulfill its obligations under the Grant Agreement and be responsible for the performance of the Project.

- F. Obtain any and all permits, licenses, and approvals required for performing any work under this Grant Agreement, including those necessary to perform design, construction, or operation and maintenance of the Project. Grantee shall provide copies of permits and approvals to State.
- G. Be solely responsible for design, construction, and operation and maintenance of projects within the work plan. Review or approval of plans, specifications, bid documents, or other construction documents by State is solely for the purpose of proper administration of funds by State and shall not be deemed to relieve or restrict responsibilities of Grantee under this Agreement.
- H. Be solely responsible for all work and for persons or entities engaged in work performed pursuant to this Agreement, including, but not limited to, contractors, subcontractors, suppliers, and providers of services. The Grantee shall be responsible for any and all disputes arising out of its contracts for work on the Project, including but not limited to payment disputes with contractors and subcontractors. The State will not mediate disputes between the Grantee and any other entity concerning responsibility for performance of work.
- D.20. GOVERNING LAW: This Grant Agreement is governed by and shall be interpreted in accordance with the laws of the State of California.
- D.21. INCOME RESTRICTIONS: The Grantee agrees that any refunds, rebates, credits, or other amounts (including any interest thereon) accruing to or received by the Grantee under this Agreement shall be paid by the Grantee to the State, to the extent that they are properly allocable to costs for which the Grantee has been reimbursed by the State under this Agreement. The Grantee shall also include in each of its contracts for work under this Agreement a provision that incorporates the requirements stated within this Paragraph.
- D.22. INDEMNIFICATION: Grantee shall indemnify and hold and save the State, its officers, agents, and employees, free and harmless from any and all liabilities for any claims and damages (including inverse condemnation) that may arise out of the Project and this Agreement, including, but not limited to any claims or damages arising from planning, design, construction, maintenance and/or operation of levee rehabilitation measures for this Project and any breach of this Agreement. Grantee shall require its contractors or subcontractors to name the State, its officers, agents and employees as additional insureds on their liability insurance for activities undertaken pursuant to this Agreement.
- D.23. INDEPENDENT CAPACITY: Grantee, and the agents and employees of Grantees, in the performance of the Grant Agreement, shall act in an independent capacity and not as officers, employees, or agents of the State.
- D.24. INSPECTION OF BOOKS, RECORDS, AND REPORTS: During regular office hours, each of the parties hereto and their duly authorized representatives shall have the right to inspect and to make copies of any books, records, or reports of either party pertaining to this Grant Agreement or matters related hereto. Each of the parties hereto shall maintain and shall make available at all times for such inspection accurate records of all its costs, disbursements, and receipts with respect to its activities under this Grant Agreement. Failure or refusal by Grantee to comply with this provision shall be considered a breach of this Grant Agreement, and State may withhold disbursements to Grantee or take any other action it deems necessary to protect its interests.
- D.25. INSPECTIONS OF PROJECT BY STATE: State shall have the right to inspect the work being performed at any and all reasonable times during the term of the Grant Agreement. This right shall extend to any subcontracts, and Grantee shall include provisions ensuring such access in all its contracts or subcontracts entered into pursuant to its Grant Agreement with State.
- D.26. LABOR CODE COMPLIANCE: The Grantee agrees to be bound by all the provisions of the Labor Code regarding prevailing wages and shall monitor all contracts subject to reimbursement from this Agreement to assure that the prevailing wage provisions of the Labor Code are being met. Current

Department of Industrial Relations (DIR) requirements may be found at: <http://www.dir.ca.gov/lcp.asp>. For more information, please refer to DIR's *Public Works Manual* at: <https://www.dir.ca.gov/dlse/PWManualCombined.pdf>. The Grantee affirms that it is aware of the provisions of section 3700 of the Labor Code, which requires every employer to be insured against liability for workers' compensation or to undertake self-insurance, and the Grantee affirms that it will comply with such provisions before commencing the performance of the work under this Agreement and will make its contractors and subcontractors aware of this provision.

- D.27. **MODIFICATION OF OVERALL WORK PLAN:** At the request of the Grantee, the State may at its sole discretion approve non-material changes to the portions of Exhibits A, B, and C which concern the budget and schedule without formally amending this Grant Agreement. Non-material changes with respect to the budget are changes that only result in reallocation of the budget and will not result in an increase in the amount of the State Grant Agreement. Non-material changes with respect to the Project schedule are changes that will not extend the term of this Grant Agreement. Requests for non-material changes to the budget and schedule must be submitted by the Grantee to the State in writing and are not effective unless and until specifically approved by the State's Program Manager in writing.
- D.28. **NONDISCRIMINATION:** During the performance of this Grant Agreement, Grantee and its contractors or subcontractors shall not unlawfully discriminate, harass, or allow harassment against any employee or applicant for employment because of sex (gender), sexual orientation, gender identity, race, color, ancestry, religion, creed, national origin (including language use restriction), pregnancy, physical disability (including HIV and AIDS), mental disability, medical condition (cancer/genetic characteristics), age (over 40), marital/domestic partner status, and denial of medical and family care leave or pregnancy disability leave. Grantee and its contractors or subcontractors shall ensure that the evaluation and treatment of their employees and applicants for employment are free from such discrimination and harassment. Grantee and its contractors or subcontractors shall comply with the provisions of the California Fair Employment and Housing Act (Gov. Code, § 12990.) and the applicable regulations promulgated there under (Cal. Code Regs., tit. 2, § 11000 et seq.). The applicable regulations of the Fair Employment and Housing are incorporated into this Agreement by reference. Grantee and its contractors or subcontractors shall give written notice of their obligations under this clause to labor organizations with which they have a collective bargaining or other Agreement.
Grantee shall include the nondiscrimination and compliance provisions of this clause in all subcontracts to perform work under the Grant Agreement.
- D.29. **OPINIONS AND DETERMINATIONS:** Where the terms of this Grant Agreement provide for action to be based upon, judgment, approval, review, or determination of either party hereto, such terms are not intended to be and shall never be construed as permitting such opinion, judgment, approval, review, or determination to be arbitrary, capricious, or unreasonable.
- D.30. **PERFORMANCE BOND:** Where contractors are used, the Grantee shall not authorize construction to begin until each contractor has furnished a performance bond in favor of the Grantee in the following amounts: faithful performance (100%) of contract value, and labor and materials (100%) of contract value. This requirement shall not apply to any contract for less than \$25,000.00. Any bond issued pursuant to this paragraph must be issued by a California-admitted surety. (Pub. Contract Code, § 7103; Code Civ. Proc., § 995.311.)
- D.31. **PRIORITY HIRING CONSIDERATIONS:** If this Grant Agreement includes services in excess of \$200,000, the Grantee shall give priority consideration in filling vacancies in positions funded by the Grant Agreement to qualified recipients of aid under Welfare and Institutions Code section 11200 in accordance with Public Contract Code section 10353.

- D.32. PROHIBITION AGAINST DISPOSAL OF PROJECT WITHOUT STATE PERMISSION: The Grantee shall not sell, abandon, lease, transfer, exchange, mortgage, hypothecate, or encumber in any manner whatsoever all or any portion of any real or other property necessarily connected or used in conjunction with the Project, or with Grantee's service of water, without prior permission of State. Grantee shall not take any action, including but not limited to actions relating to user fees, charges, and assessments that could adversely affect the ability of Grantee meet its obligations under this Grant Agreement, without prior written permission of State. State may require that the proceeds from the disposition of any real or personal property be remitted to State.
- D.33. PROJECT ACCESS: The Grantee shall ensure that the State, the Governor of the State, or any authorized representative of the foregoing, will have safe and suitable access to the Project site at all reasonable times during Project construction and thereafter for the term of this Agreement.
- D.34. REMAINING BALANCE: In the event the Grantee does not submit invoices requesting all of the funds encumbered under this Grant Agreement, any remaining funds revert to the State. The State will notify the Grantee stating that the Project file is closed and any remaining balance will be disencumbered and unavailable for further use under this Grant Agreement.
- D.35. REMEDIES NOT EXCLUSIVE: The use by either party of any remedy specified herein for the enforcement of this Grant Agreement is not exclusive and shall not deprive the party using such remedy of, or limit the application of, any other remedy provided by law.
- D.36. RETENTION: The State shall withhold ten percent (10%) of the funds, for each project, until the project is complete, and a Final Project Report is approved and accepted by DWR. If a project has multiple components (within a project), at the State's discretion and upon a written request by the Grantee, any retained amount attributable to a single component may be released when that component is complete and the Final Component Completion Report is approved. Upon approval of the Final Project Report and/or Final Component Completion Report, any retained amounts due to the Grantee will be promptly disbursed to the Grantee, without interest.
- D.37. RIGHTS IN DATA: Grantee agrees that all data, plans, drawings, specifications, reports, computer programs, operating manuals, notes and other written or graphic work produced in the performance of this Grant Agreement shall be made available to the State and shall be in the public domain to the extent to which release of such materials is required under the California Public Records Act. (Gov. Code, § 6250 et seq.) Grantee may disclose, disseminate and use in whole or in part, any final form data and information received, collected and developed under this Grant Agreement, subject to appropriate acknowledgement of credit to State for financial support. Grantee shall not utilize the materials for any profit-making venture or sell or grant rights to a third party who intends to do so. The State shall have the right to use any data described in this paragraph for any public purpose.
- D.38. SEVERABILITY: Should any portion of this Grant Agreement be determined to be void or unenforceable, such shall be severed from the whole and the Grant Agreement shall continue as modified.
- D.39. SUSPENSION OF PAYMENTS: This Grant Agreement may be subject to suspension of payments or termination, or both if the State determines that:
- A. Grantee, its contractors, or subcontractors have made a false certification, or
 - B. Grantee, its contractors, or subcontractors violates the certification by failing to carry out the requirements noted in this Grant Agreement.
- D.40. SUCCESSORS AND ASSIGNS: This Grant Agreement and all of its provisions shall apply to and bind the successors and assigns of the parties. No assignment or transfer of this Grant Agreement or any

part thereof, rights hereunder, or interest herein by the Grantee shall be valid unless and until it is approved by State and made subject to such reasonable terms and conditions as State may impose.

- D.41. TERMINATION BY GRANTEE: Subject to State approval which may be reasonably withheld, Grantee may terminate this Agreement and be relieved of contractual obligations. In doing so, Grantee must provide a reason(s) for termination. Grantee must submit all progress reports summarizing accomplishments up until termination date.
- D.42. TERMINATION FOR CAUSE: Subject to the right to cure under Paragraph 12, "Default Provisions," the State may terminate this Grant Agreement and be relieved of any payments should Grantee fail to perform the requirements of this Grant Agreement at the time and in the manner herein, provided including but not limited to reasons of default under Paragraph 12, "Default Provisions."
- D.43. TERMINATION WITHOUT CAUSE: The State may terminate this Agreement without cause on 30 days' advance written notice. The Grantee shall be reimbursed for all reasonable expenses incurred up to the date of termination.
- D.44. THIRD PARTY BENEFICIARIES: The parties to this Agreement do not intend to create rights in, or grant remedies to, any third party as a beneficiary of this Agreement, or any duty, covenant, obligation or understanding established herein.
- D.45. TIMELINESS: Time is of the essence in this Grant Agreement.
- D.46. TRAVEL – DAC, EDA, TRIBES PROJECT: Travel is only an eligible reimbursable expense for projects providing at least 75% of benefits to DACs, EDAs, and/or Tribes (based on population or geographic area). Only ground transportation and lodging are eligible for grant reimbursement. Per diem costs will not be eligible for grant reimbursement. Any reimbursement for necessary travel shall be at rates not to exceed those set by the California Department of Human Resources. These rates may be found at: <http://www.calhr.ca.gov/employees/Pages/travel-reimbursements.aspx>. Reimbursement will be at the State travel amounts that are current as of the date costs are incurred. No travel outside of the IRWM region shall be reimbursed unless prior written authorization is obtained from the State.
- D.47. UNION ORGANIZING: Grantee, by signing this Grant Agreement, hereby acknowledges the applicability of Government Code sections 16645 through 16649 to this Grant Agreement. Furthermore, Grantee, by signing this Grant Agreement, hereby certifies that:
- A. No State funds disbursed by this Grant Agreement will be used to assist, promote, or deter union organizing.
 - B. Grantee shall account for State funds disbursed for a specific expenditure by this Grant Agreement to show those funds were allocated to that expenditure.
 - C. Grantee shall, where State funds are not designated as described in (b) above, allocate, on a pro rata basis, all disbursements that support the program.
 - D. If Grantee makes expenditures to assist, promote, or deter union organizing, Grantee will maintain records sufficient to show that no State funds were used for those expenditures and that Grantee shall provide those records to the Attorney General upon request.
- D.48. VENUE: The State and the Grantee hereby agree that any action arising out of this Agreement shall be filed and maintained in the Superior Court in and for the County of Sacramento, California, or in the United States District Court in and for the Eastern District of California. The Grantee hereby waives any existing sovereign immunity for the purposes of this Agreement.
- D.49. WAIVER OF RIGHTS: None of the provisions of this Grant Agreement shall be deemed waived unless expressly waived in writing. It is the intention of the parties here to that from time to time either party

may waive any of its rights under this Grant Agreement unless contrary to law. Any waiver by either party of rights arising in connection with the Grant Agreement shall not be deemed to be a waiver with respect to any other rights or matters, and such provisions shall continue in full force and effect.

EXHIBIT E
AUTHORIZING RESOLUTION



Coachella Valley Water District
Board of Directors

Resolution No: 2022-33

RESOLUTION OF THE BOARD OF DIRECTORS OF COACHELLA VALLEY WATER DISTRICT AUTHORIZING THE GENERAL MANAGER OR HIS DESIGNEE TO SUBMIT A ROUND 2 INTEGRATED REGIONAL WATER MANAGEMENT IMPLEMENTATION GRANT APPLICATION FOR \$4,112,755, ACCEPT THE GRANT FUNDS THAT ARE AWARDED, ENTER INTO CONTRACTS TO DISTRIBUTE THE FUNDS TO PROJECT SPONSORS, AND SERVE AS LEAD AGENCY FOR CALIFORNIA ENVIRONMENTAL QUALITY ACT COMPLIANCE AS NECESSARY

WHEREAS, Proposition 1, the Water Quality, Supply, and Infrastructure Improvement Act of 2014 (Water Code Section 79700 *et seq.*), authorized the California Legislature to appropriate \$510 million to encourage integrated regional water management planning in California; and

WHEREAS, Section 79744(a) of the California Water Code appropriated to the Department of Water Resources funds for integrated regional water management programs, projects and other purposes; and

WHEREAS, DWR is making these funds available through several grant programs; and

WHEREAS, achieving Integrated Regional Water Management (IRWM) grant funding will help to achieve the regional water supply goals established in the 2020 Coachella Valley Regional Urban Water Management Plan and the groundwater sustainability goals established in the Sustainable Groundwater Management Act, and to prepare the Coachella Valley Region for the impacts of drought; and

WHEREAS, the Coachella Valley Water Management Group will prepare an application for a Round 2 Integrated Regional Water Management Implementation Grant to support the development of high-priority water management projects in the Coachella Valley Region; and

WHEREAS, on June 21, 2022, the Coachella Valley Water Management Group and Coachella Valley Planning Partners recommended the Coachella Valley Water District Board authorize submittal of Coachella Valley Region's application for a Round 2 Integrated Regional Water Management Implementation Grant; and

WHEREAS, the memorandum of understanding that established the Coachella Valley IRWM Program identifies the Coachella Valley Water District as the program's authorized representative; and

**Coachella Valley Water District
Board of Directors**

Resolution No: 2022-33

WHEREAS, the Coachella Valley Water District Board of Directors is the decision-making body for the Coachella Valley Water District; and

WHEREAS, grant application procedures established by DWR require applicants to provide a copy of a resolution adopted by the applicant's governing body designating an authorized representative to file an application for an IRWM planning grant.

WHEREAS, the Colorado River Funding Area (CRFA) Regional Water Management Groups (RWMGs) have entered into a Memorandum of Understanding setting forth the division of the grant funds between the CRFA; and

WHEREAS, the Coachella Valley RWMG, of which Coachella Valley Water District is a member agency, is allocated \$4.1 million for projects in the Coachella Valley.

NOW, THEREFORE, BE IT RESOLVED by the Board of Directors of the District as follows:

1. The General Manager or his designee is authorized to prepare the necessary data, conduct investigations and submit a Proposition 1, Round 2 Integrated Regional Water Management Implementation Grant application.
2. The General Manager or his designee is authorized to execute a grant agreement or any amendments thereto to receive a Proposition 1, Round 2 Integrated Regional Water Management Implementation Grant from the California Department of Water Resources.
3. The General Manager or his designee is authorized to accept the grant funds that are awarded, enter into contracts to distribute the awarded grant funds to the project sponsors, and sign all necessary documentation (e.g. invoices, progress reports, etc.).

PASSED and ADOPTED by the Coachella Valley Water District Board of Directors during a regular meeting on this 26th day of July 2022, by the following vote:

AYES: Powell, Nelson, Aguilar, Bianco

NOES: None

ABSENT: Estrada



Sylvia M. Bernandez, MMC
Clerk of the Board
Coachella Valley Water District



EXHIBIT F

REPORT FORMATS AND REQUIREMENTS

The following reporting formats should be utilized. Please obtain State approval prior to submitting a report in an alternative format.

PROGRESS REPORTS

Progress reports shall generally use the following format. This format may be modified as necessary to effectively communicate information. For each project, discuss the following at the task level, as organized in Exhibit A:

- Percent complete (by work)
- Discussion of work accomplished during the reporting period.
- Milestones or deliverables completed/submitted during the reporting period.
- Meetings held or attended.
- Scheduling concerns and issues encountered that may delay completion of the task.

For each project, discuss the following at the project level, as organized in Exhibit A:

- Work anticipated for the next reporting period.
- Photo documentation, as appropriate.
- Budget projections for grant share for the next two quarters
- Any schedule or budget modifications approved by DWR during the reporting period.

PROJECT COMPLETION REPORT

The Project Completion Report (or a Component Completion Report, if a Project has multiple Components) shall generally use the following format provided below for each project after completion.

Executive Summary

The Executive Summary should include a brief summary of project information and include the following items:

- Brief description of work proposed to be done in the original Grant application.
- List any official amendments to this Grant Agreement, with a short description of the amendment.

Reports and/or Products

The following items should be provided, unless already submitted as a deliverable:

- A copy of any final technical report or study, produced for or utilized in this Project as described in the Exhibit A
- Electronic copies of any data collected, not previously submitted
- Discussion of problems that occurred during the work and how those problems were resolved
- Final project schedule showing actual progress versus planned progress as shown in Exhibit C

Additional information that may be applicable for implementation projects includes the following:

- Record drawings
- Final geodetic survey information

- Project photos

Cost & Disposition of Funds

A list showing:

- Summary of Project costs including the following items:
 - Accounting of the cost of project expenditure;
 - Include all internal and external costs not previously disclosed (i.e., additional cost share); and
 - A discussion of factors that positively or negatively affected the project cost and any deviation from the original Project cost estimate.

Additional Information

- Benefits derived from the Project, with quantification of such benefits provided.
- If applicable, Certification from a California Registered Professional (Civil Engineer or Geologist, as appropriate), consistent with Exhibit D, that the project was conducted in accordance with the approved Work Plan in Exhibit A and any approved amendments thereto.
- Submittal schedule for the Post-Performance Report.

GRANT COMPLETION REPORT

The Grant Completion Report shall generally use the following format. This format may be modified as necessary to effectively communicate information on the various projects funded by this Grant Agreement, and includes the following:

- Executive Summary: consisting of a maximum of ten (10) pages summarizing information for the grant as well as the individual projects.
- Brief discussion of: each project completed and how they achieved IRWM Plan objectives and/or Regional goals and whether the level, type, or magnitude of benefits of the project are comparable to the original project proposal; any remaining work to be completed and mechanism for their implementation; the benefits to DAC and/or EDA as part of this Grant Agreement if a DAC or EDA Cost Share Waiver was approved for a project; and a summary of final funds disbursement for each project.

Additional Information: Summary of the submittal schedule for the Post-Performance Reports applicable for the projects in this Grant Agreement.

POST-PERFORMANCE REPORT

The Post-Performance Report (PPR) should be concise and focus on how each project is performing compared to its expected performance; whether the project is being operated and maintained and providing intended benefits as proposed. A PPR template may be provided by the assigned DWR Grant Manager upon request. The PPR should follow the general format of the template and provide requested information as applicable. The following information, at a minimum, shall be provided:

Reports and/or products

- Header including the following:
 - Grantee Name
 - Implementing Agency (if different from Grantee)
 - Grant Agreement Number
 - Project Name
 - Funding grant source (i.e., 2022 Proposition 1 IRWM Implementation Grant)
 - Report number

- Post-Performance Report schedule
- Time period of the annual report (e.g., January 2024 through December 2024)
- Project Description Summary
- Discussion of the project benefits
- An assessment of any differences between the expected versus actual project benefits as stated in the original application. Where applicable, the reporting should include quantitative metrics (e.g., new acre-feet of water produced that year, etc.).
- Summary of any additional costs and/or benefits deriving from the project since its completion, if applicable.
- Any additional information relevant to or generated by the continued operation of the project.

EXHIBIT G

REQUIREMENTS FOR DATA SUBMITTAL

Surface and Groundwater Quality Data:

Groundwater quality and ambient surface water quality monitoring data that include chemical, physical, or biological data shall be submitted to the State as described below, with a narrative description of data submittal activities included in project reports.

Surface water quality monitoring data shall be prepared for submission to the California Environmental Data Exchange Network (CEDEN). The CEDEN data templates are available on the CEDEN website. Inclusion of additional data elements described on the data templates is desirable. Data ready for submission should be uploaded to your CEDEN Regional Data Center via the CEDEN website. CEDEN website: <http://www.ceden.org>.

If a project's Work Plan contains a groundwater ambient monitoring element, groundwater quality monitoring data shall be submitted to the State for inclusion in the State Water Resources Control Board's Groundwater Ambient Monitoring and Assessment (GAMA) Program Information on the GAMA Program can be obtained at: https://www.waterboards.ca.gov/water_issues/programs/gama/. If further information is required, the Grantee can contact the State Water Resources Control Board (SWRCB) GAMA Program. A listing of SWRCB staff involved in the GAMA program can be found at: https://www.waterboards.ca.gov/water_issues/programs/gama/contact.shtml.

Groundwater Level Data

For each project that collects groundwater level data, the Grantee will need to submit this data to DWR's Water Data Library (WDL), with a narrative description of data submittal activities included in project reports, as described in Exhibit F, "Report Formats and Requirements." Information regarding the WDL and in what format to submit data in can be found at: <http://www.water.ca.gov/waterdatalibrary/>.

EXHIBIT H

STATE AUDIT DOCUMENT REQUIREMENTS AND COST SHARE GUIDELINES FOR THE GRANTEE

The following provides a list of documents typically required by State Auditors and general guidelines for the Grantee. List of documents pertains to both State funding and the Grantee's Local Cost Share and details the documents/records that State Auditors would need to review in the event of this Grant Agreement is audited. The Grantee should ensure that such records are maintained for each funded project.

State Audit Document Requirements

Internal Controls

1. Organization chart (e.g., Agency's overall organization chart and organization chart for the State funded Program/Project).
2. Written internal procedures and flowcharts for the following:
 - a) Receipts and deposits
 - b) Disbursements
 - c) State reimbursement requests
 - d) Expenditure tracking of State funds
 - e) Guidelines, policy, and procedures on State funded Program/Project
3. Audit reports of the Agency internal control structure and/or financial statements within the last two years.
4. Prior audit reports on the State funded Program/Project.

State Funding:

1. Original Grant Agreement, any amendment(s) and budget modification documents.
2. A listing of all bond-funded grants, loans, or subventions received from the State.
3. A listing of all other funding sources for each Program/Project.

Contracts:

1. All subcontractor and consultant contracts and related or partners' documents, if applicable.
2. Contracts between the Agency and member agencies as related to the State funded Program/Project.

Invoices:

1. Invoices from vendors and subcontractors for expenditures submitted to the State for payments under the Grant Agreement.
2. Documentation linking subcontractor invoices to State reimbursement, requests and related Grant Agreement budget line items.
3. Reimbursement requests submitted to the State for the Grant Agreement.

Cash Documents:

1. Receipts (copies of warrants) showing payments received from the State.
2. Deposit slips (or bank statements) showing deposit of the payments received from the State.
3. Cancelled checks or disbursement documents showing payments made to vendors, subcontractors, consultants, and/or agents under the grants or loans.
4. Bank statements showing the deposit of the receipts.

Accounting Records:

1. Ledgers showing entries for funding receipts and cash disbursements.
2. Ledgers showing receipts and cash disbursement entries of other funding sources.
3. Bridging documents that tie the general ledger to requests for Grant Agreement reimbursement.

Administration Costs:

1. Supporting documents showing the calculation of administration costs.

Personnel:

1. List of all contractors and Agency staff that worked on the State funded Program/Project.
2. Payroll records including timesheets for contractor staff and the Agency personnel who provided services charged to the program

Project Files:

1. All supporting documentation maintained in the project files.
2. All Grant Agreement related correspondence.

Cost Share Guidelines

Cost Share consists of non-State funds, including in-kind services. In-kind services are defined as work performed (i.e., dollar value of non-cash contributions) by the Grantee (and potentially other parties) directly related to the execution of the funded project. Examples include volunteer services, equipment use, and use of facilities. The cost if in-kind service can be counted as cost share in-lieu of actual funds (or revenue) provided by the Grantee. Other cost share and in-kind service eligibility conditions may apply. Provided below is guidance for documenting cost share with and without in-kind services.

1. Although tracked separately, in-kind services shall be documented and, to the extent feasible, supported by the same methods used by the Grantee for its own employees. Such documentation should include the following:
 - a. Detailed description of the contributed item(s) or service(s)
 - b. Purpose for which the contribution was made (tied to project work plan)
 - c. Name of contributing organization and date of contribution
 - d. Real or approximate value of contribution. Who valued the contribution and how was the value determined? (e.g., actual, appraisal, fair market, etc.). Justification of rate. (See item #2, below)
 - e. Person's name and the function of the contributing person
 - f. Number of hours contributed
 - g. If multiple sources exist, these should be summarized on a table with summed charges
 - h. Source of contribution if it was provided by, obtained with, or supported by government funds
2. Rates for volunteer or in-kind services shall be consistent with those paid for similar work in the Grantee's organization. For example, volunteer service of clearing vegetation performed by an attorney shall be valued at fair market value for this service, not the rate for professional legal services. In those instances, in which the required skills are not found in the recipient organization, rates shall be consistent with those paid for similar work in the labor market. Paid fringe benefits that are reasonable, allowable, and allocable may be included in the valuation.
3. Cost share contribution (including in-kind services) shall be for costs and services directly attributed to activities included in the Grant Agreement. These services, furnished by professional and technical personnel, consultants, and other skilled labor may be counted as in-kind if the activities are an integral and necessary part of the project funded by the Grant Agreement.
4. Cash contributions made to a project shall be documented as revenue and in-kind services as expenditures. These costs should be tracked separately in the Grantee's accounting system.

EXHIBIT I

LOCAL PROJECT SPONSORS AND PROJECT LOCATIONS

The Grantee has assigned, for each project, a Local Project Sponsor (LPS) according to the roles of the participating agencies identified in the IRWM Plan. LPSs may act on behalf of the Grantee for the purposes of individual project management, oversight, compliance, and operations and maintenance. LPSs are identified for each sponsored Project below:

Local Project Sponsor Agency Designation

Sponsored Project: Project 1: Reservoirs 4711-3 and 4711-4 Construction Project

Amendment 2: Project 1 Removed and Replaced by Project 7


Local Project Sponsor Agency Designation

Sponsored Project: Project 2: Desert Water Agency Regional Conservation Program

Sponsor Agency: Desert Water Agency

Agency Address: 1200 S. Gene Autry Trail, Palm Springs, CA, 92264

Project Location: Palm Springs and Desert Hot Springs, California
(33.83910, -116.37545, 33.947887, -116.521021, and 33.72207438006168, -116.22305356272942)

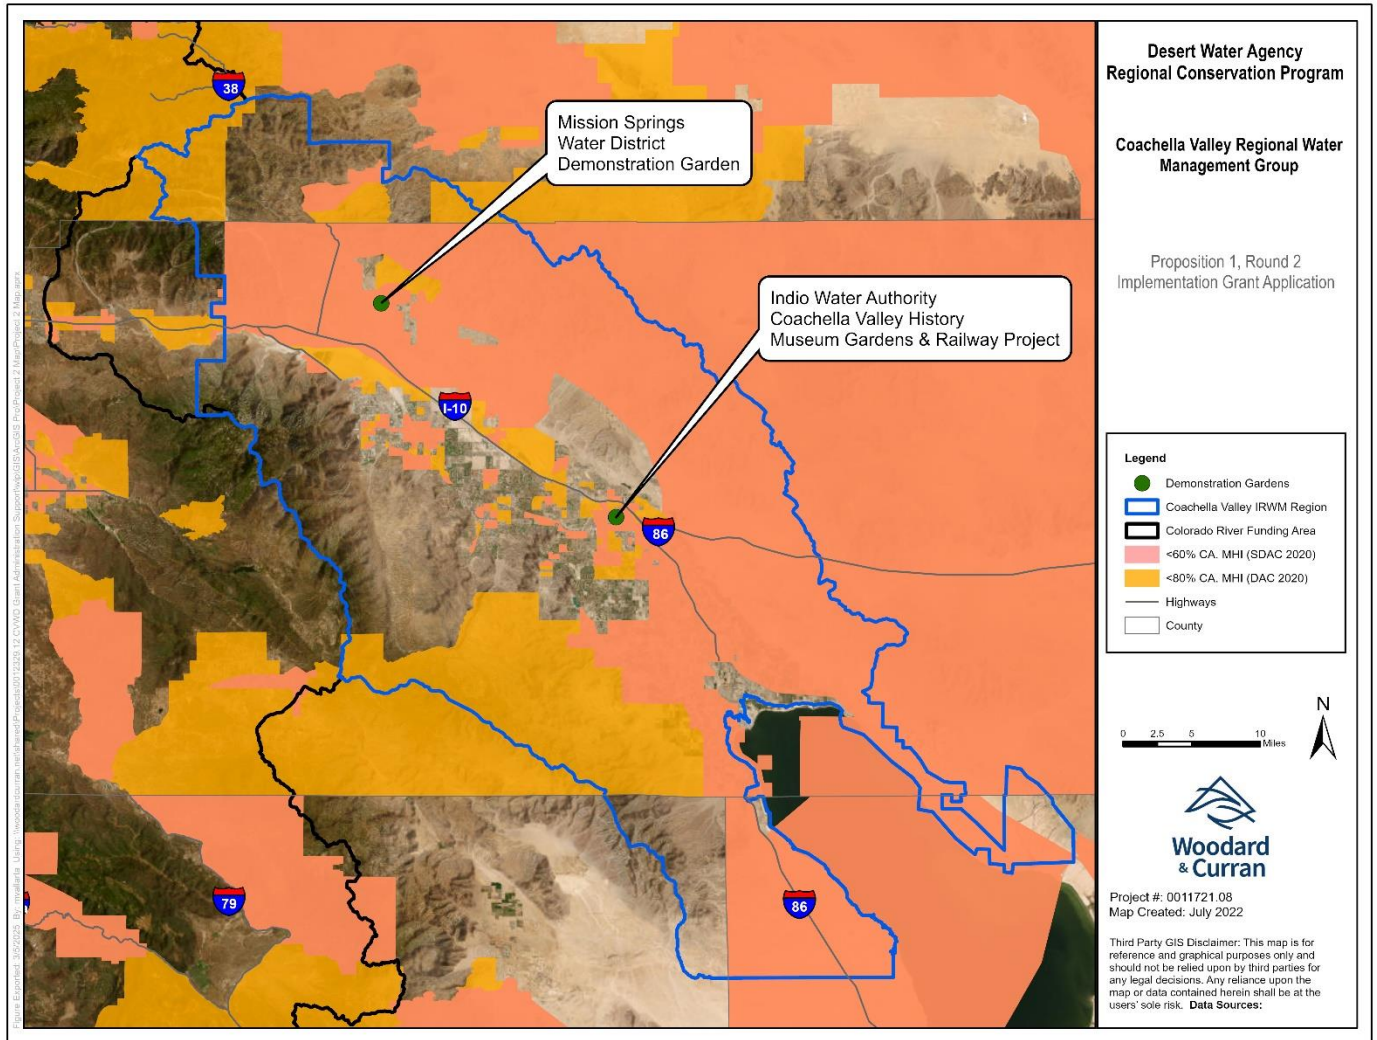


Local Project Sponsor Agency Designation

Sponsored Project: Project 3: Groundwater Quality Protection Project – Area D-3

Sponsor Agency: Mission Springs Water District

Agency Address: 66575 2nd Street, Desert Hot Springs, CA, 92240

Project Location: Desert Hot Springs, California (33.97403, -116.50332)

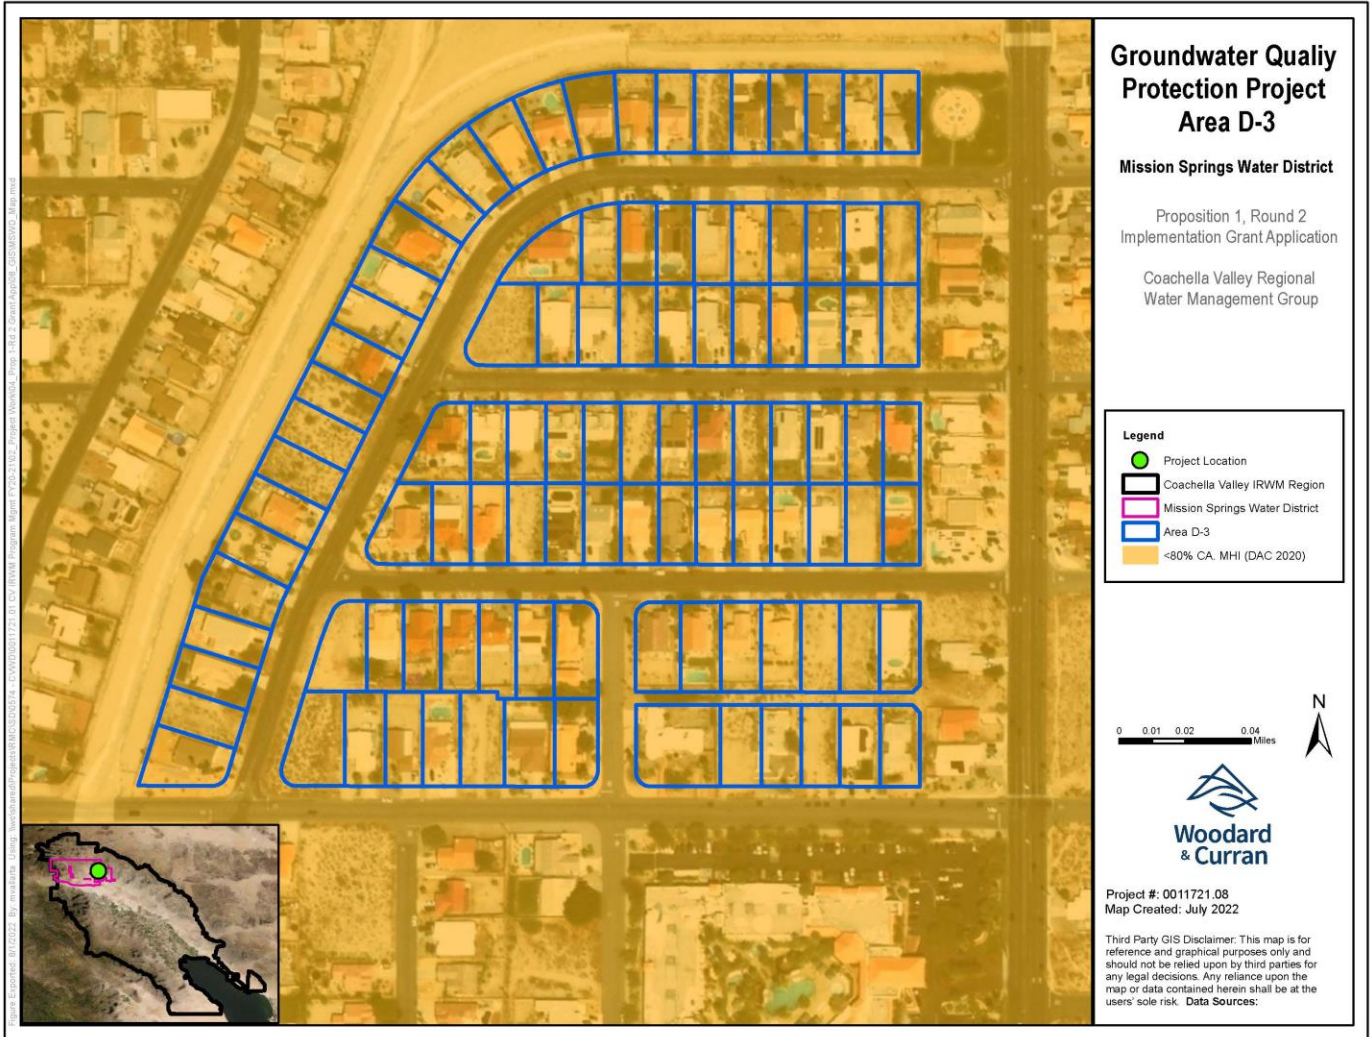


Local Project Sponsor Agency Designation

Sponsored Project: Project 4: Coachella Water Authority Groundwater Well Project

Sponsor Agency: Coachella Water Authority

Agency Address: 1515 Sixth Street, Coachella, CA, 92236

Project Location: Coachella, California (33.67323, -116.19872)

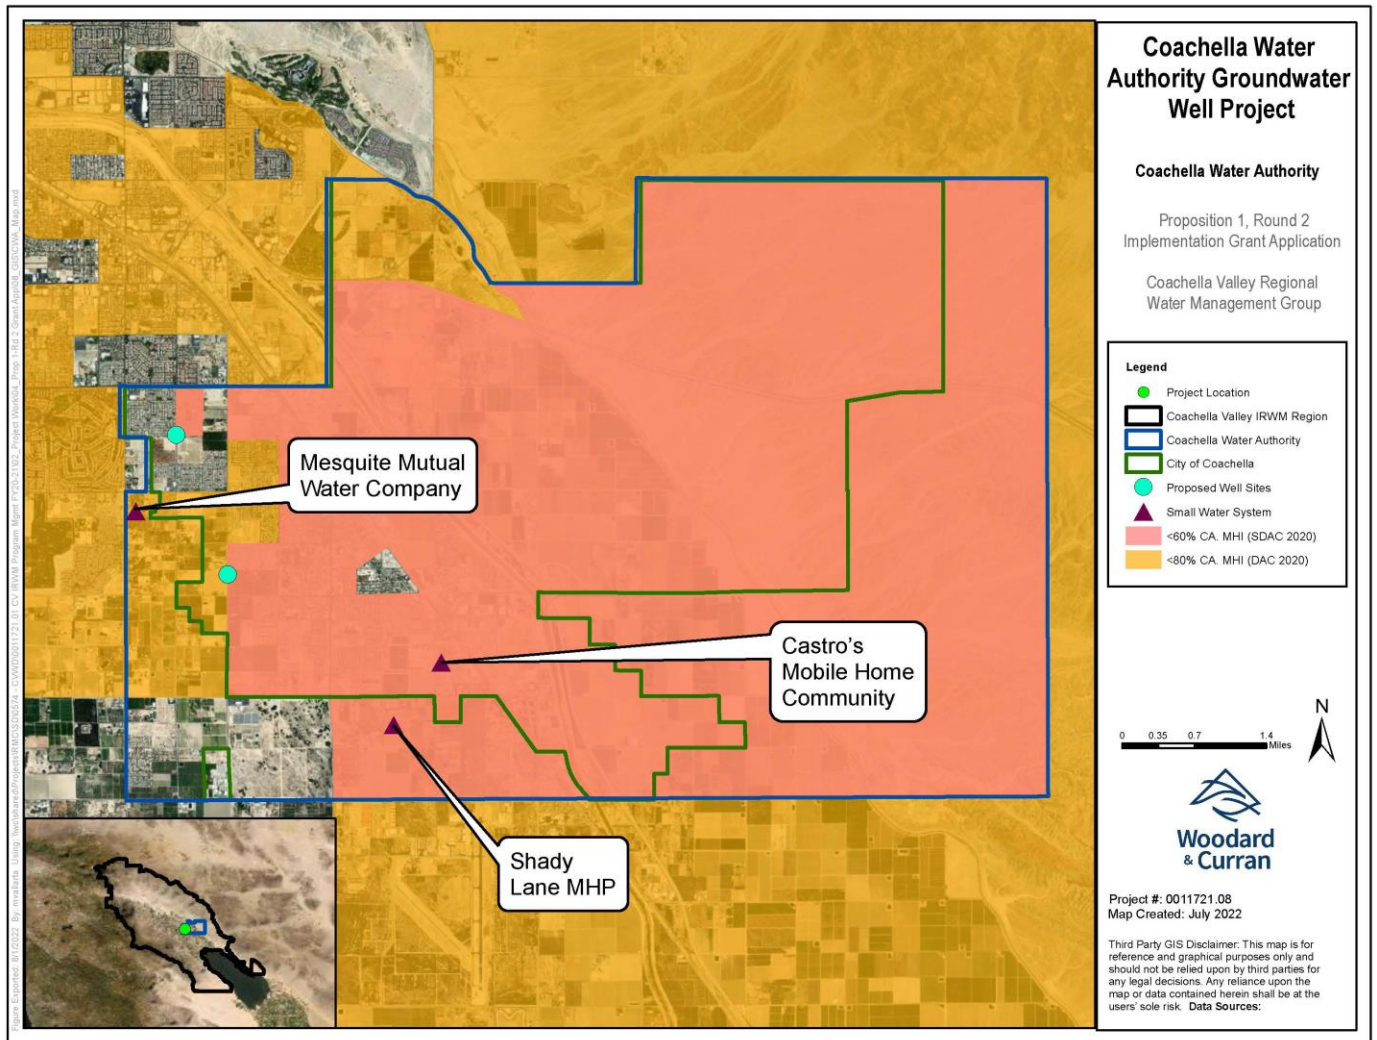

Local Project Sponsor Agency Designation

Sponsored Project: Project 5: Polanco Septic Rehabilitation Program

Amendment 2: Project 5 Removed and Replaced by Project 8


Local Project Sponsor Agency Designation

Sponsored Project: Project 6: Sunrise Park Recycled water Connection

Sponsor Agency: Desert Water Agency

Agency Address: 1200 S. Gene Autry Trail, Palm Springs, CA, 92264

Project Location: Palm Springs, California (33.81707, -116.52625)

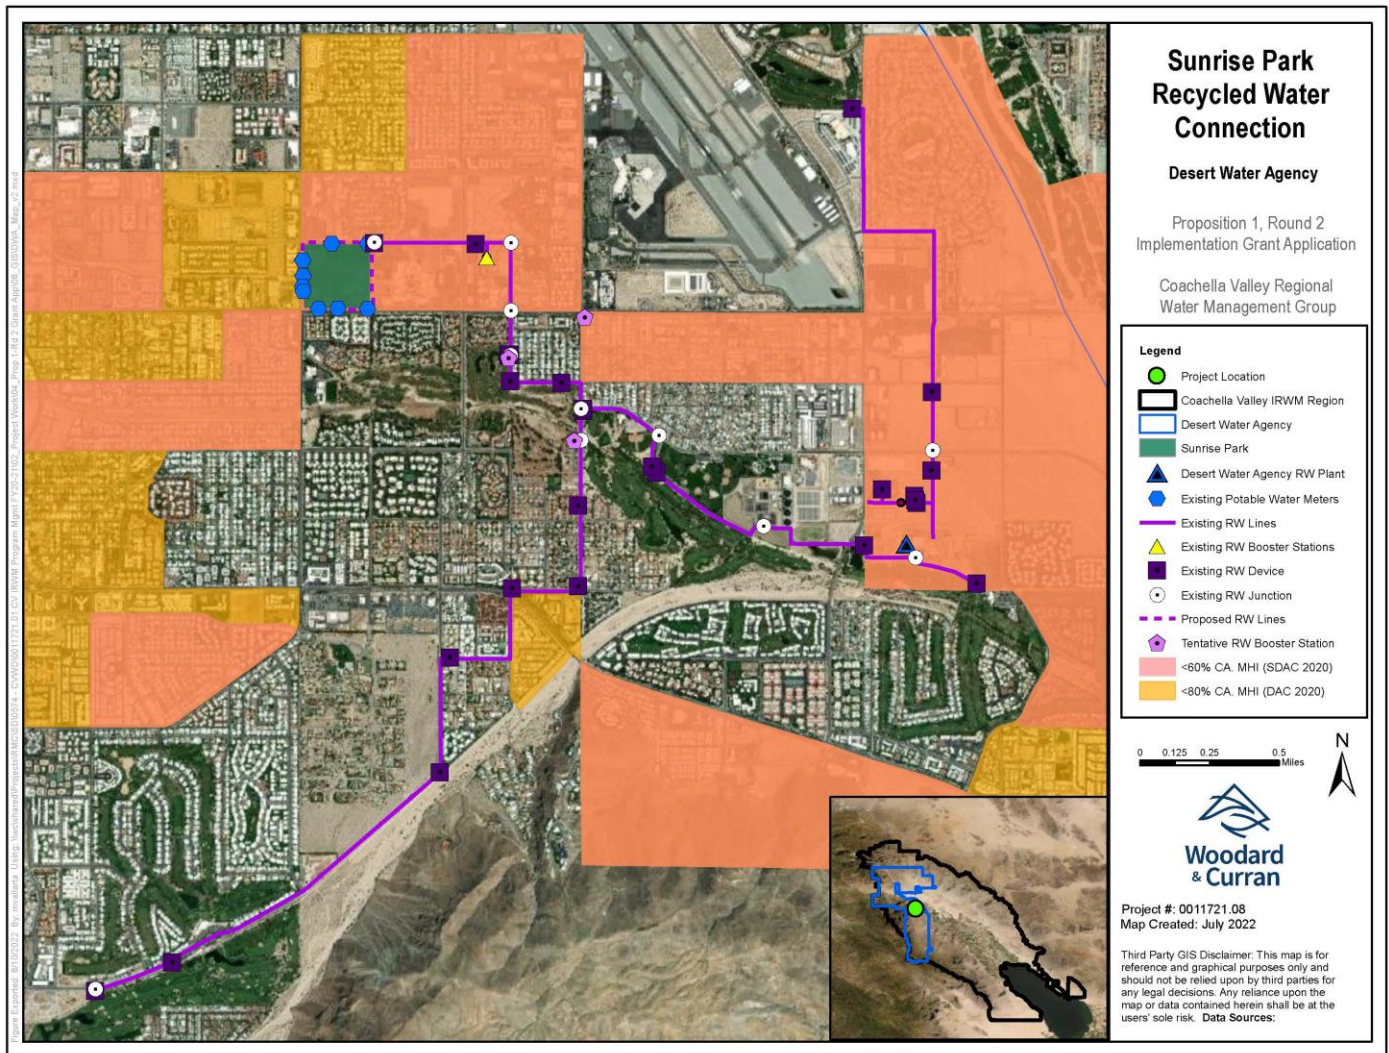


Local Project Sponsor Agency Designation

Sponsored Project: Project 7: Stannous Chloride Demonstration Testing

Sponsor Agency: Coachella Valley Water District

Agency Address: 75515 Hovley Lane East, Palm Desert, CA, 92211

Project Location: Sky Valley, California (33.9026169, -116.3656348)

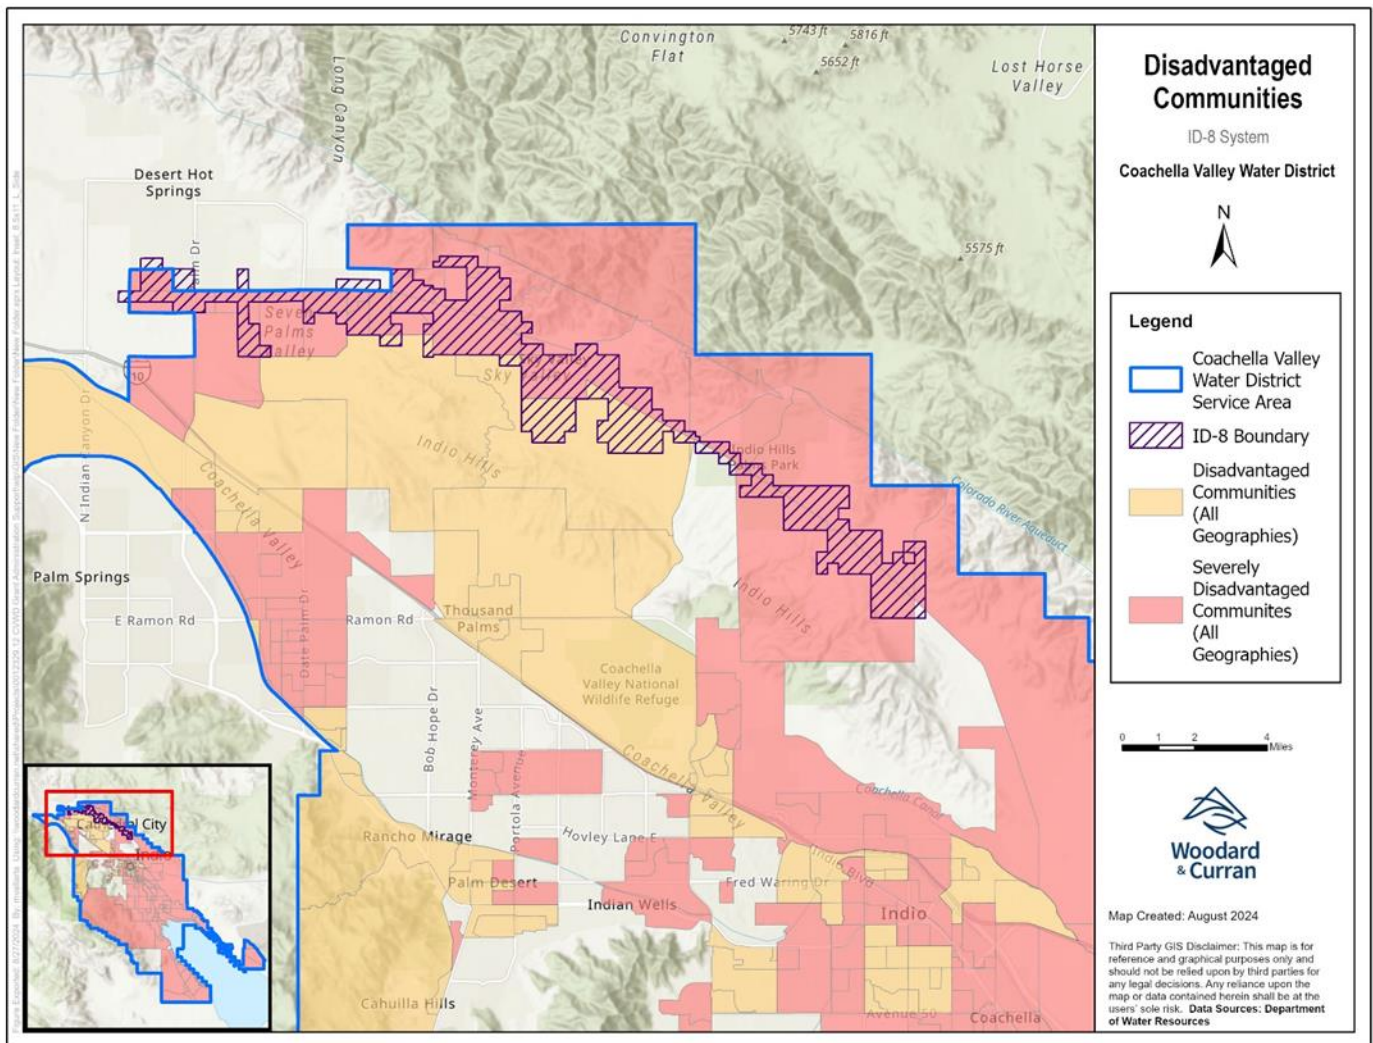

Local Project Sponsor Agency Designation

Sponsored Project: Project 8: Reservoir 7802-2 Project

Sponsor Agency: Coachella Valley Water District

Agency Address: 75515 Hovley Lane East, Palm Desert, CA, 92211

Project Location: Thermal, California (33.5499056°, -116.1915556)

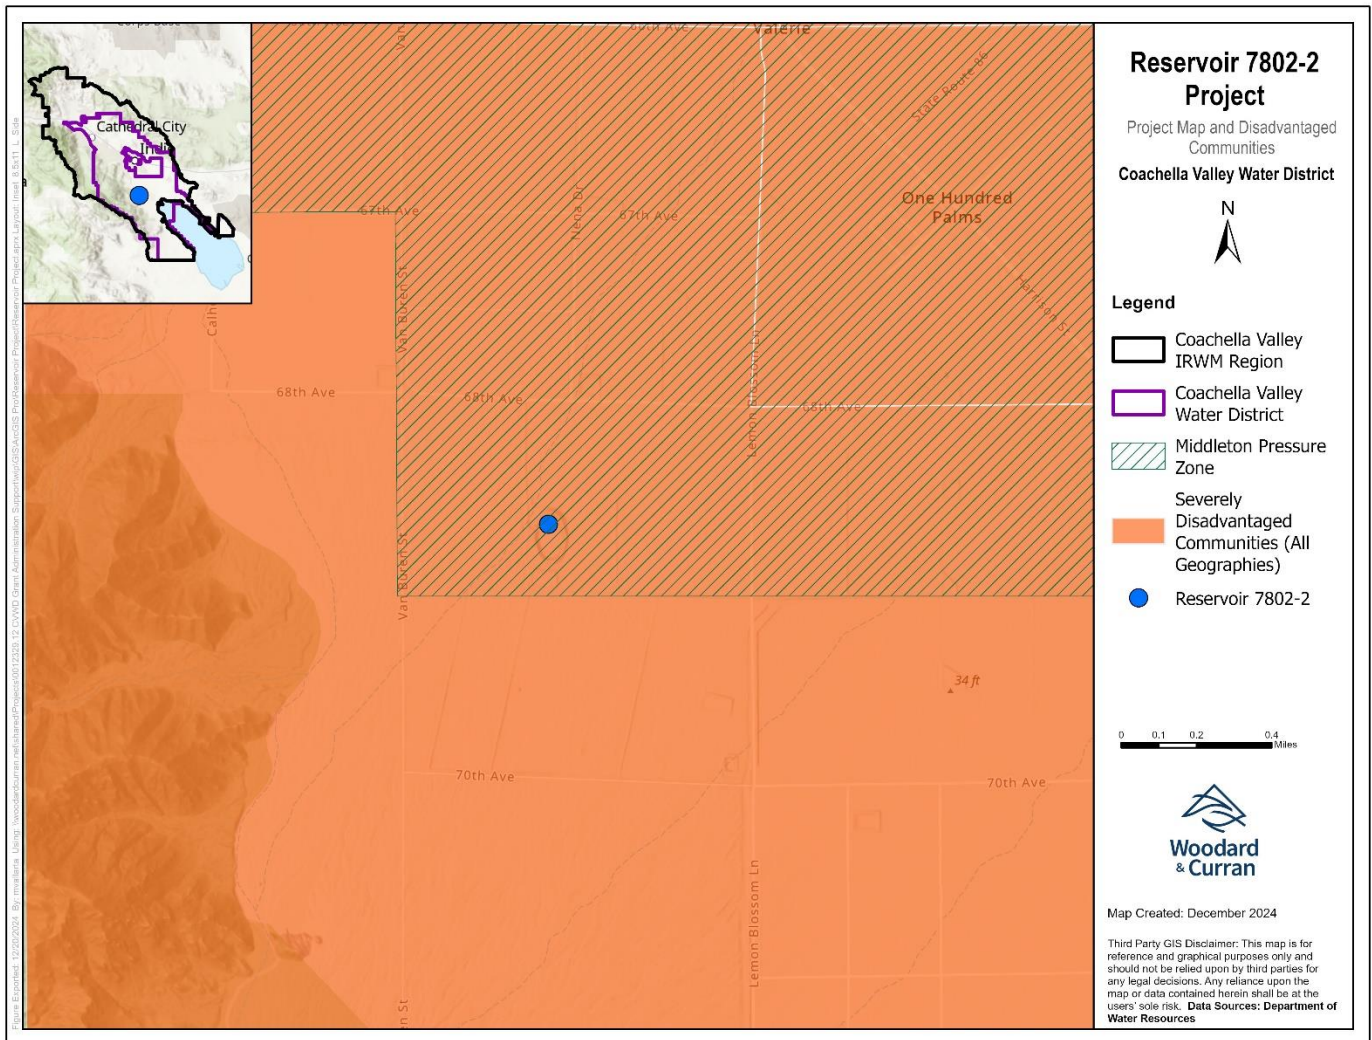


EXHIBIT J

APPRAISAL SPECIFICATIONS

For property acquisitions funded by this Grant Agreement, the Grantee shall submit an appraisal for review and approval by the Department of General Services or DWR's Real Estate Branch prior to reimbursement or depositing State funds into an escrow account. This information should be submitted at least 90 days prior to a reimbursement request to account for review time. All appraisal reports, regardless of report format, shall include all applicable Appraisal Specifications below. Appraisals for a total compensation of \$150,000 or more shall be reported as a Self-Contained Appraisal Report. Appraisals for a total compensation of less than \$150,000 may be reported as a Summary Appraisal Report, which includes all information necessary to arrive at the appraiser's conclusion. Appraisal Specifications 14, 16, 21, 23-25, and 28 shall be a narrative analysis regardless of the reporting format.

1. Title page with sufficient identification of appraisal assignment.
2. Letter of transmittal summarizing important assumptions and conclusions, value estimate, date of value and date of report.
3. Table of contents.
4. Assumptions and Limiting Conditions, Extraordinary Assumptions, and Hypothetical Conditions as needed.
5. Description of the scope of work, including the extent of data collection and limitations, if any, in obtaining relevant data.
6. Definition of Fair Market Value, as defined by California Code of Civil Procedure, § 1263.320.
7. Photographs of subject property and comparable data, including significant physical features and the interior of structural improvements, if applicable.
8. Copies of Tax Assessor's plat map with the subject marked along with all contiguous assessor's parcels that depict the ownership.
9. A legal description of the subject property, if available.
10. For large, remote or inaccessible parcels, provide aerial photographs or topographical maps depicting the subject boundaries.
11. Three (3) year subject property history, including sales, listings, leases, options, zoning, applications for permits, or other documents or facts that might indicate or affect use or value.
12. Discussion of any current Agreement of Sale, option, or listing of subject property. This issue required increased diligence since state agencies often utilize non-profit organizations to quickly acquire sensitive habitat parcels using Option Agreements. However, due to confidentiality clauses, the terms of the Option are often not disclosed to the State. If the appraiser discovers evidence of an Option or the possible existence of an Option, and the terms cannot be disclosed due to a confidentiality clause, then the appraiser is to cease work and contact the client.
13. Regional, area, and neighborhood analyses. This information may be presented in a summary format.
14. Market conditions and trends including identification of the relevant market area, a discussion of supply and demand within the relevant market area, and a discussion of the relevant market factors impacting demand for site acquisition and leasing within the relevant market area. This information may be presented in a summary format.
15. Discussion of subject land/site characteristics (size, topography, current use, elevations, zoning and land use issues, development entitlements, General Plan designation, utilities, offsite improvements,

access, land features such as levees and creeks, offsite improvements, easements and encumbrances, covenants, conditions and restrictions, flood and earthquake information, toxic hazards, water rights, mineral rights, toxic hazards, taxes and assessments, etc.).

16. Description of subject improvements including all structures, square footage, physical age, type of construction, quality of construction, condition of improvements and/or identification of any permanent plantings. Discussion of construction cost methodology, costs included and excluded, accrued depreciation from all causes, remaining economic life, items of deferred maintenance and cost to cure, and incurable items. Construction cost data shall include cost data source, date of estimate or date of publication of cost manual, section and page reference of cost manual, copies of cost estimate if provided from another source, replacement or reproduction cost method used, and supporting calculations including worksheets or spreadsheets.
17. Subject property leasing and operating cost history, including all items of income and expense.
18. Analysis and conclusion of the larger parcel for partial taking appraisals. For partial taking appraisals, Appraisal Specifications generally apply to the larger parcel rather than an ownership where the larger parcel is not the entire ownership.
19. Include a copy of a recent preliminary title report (within the past year) as an appraisal exhibit. Discuss the title exceptions and analyze the effect of title exceptions on fair market value.
20. For appraisals of partial takings or easements, a detailed description of the taking or easement area including surface features and topography, easements, encumbrances or improvements including levees within the subject partial take or easement, and whether the take area is characteristic of the larger parcel. Any characteristics of the taking area, including existing pre-project levees that render the take area different from the larger parcel shall be addressed in the valuation.
21. Opinion of highest and best use for the subject property, based on an in-depth analysis supporting the concluded use which includes the detail required by the complexity of the analysis. Such support typically requires a discussion of the four criteria of tests utilized to determine the highest and best use of a property. If alternative feasible uses exist, explain and support market, development, cash flow, and risk factors leading to an ultimate highest and best use decision.
22. All approaches to market value applicable to the property type and in the subject market. Explain and support the exclusion of any usual approaches to value.
23. Map(s) showing all comparable properties in relation to the subject property.
24. Photographs and plat maps of comparable properties.
25. In-depth discussion of comparable properties, similarities and differences compared to the subject property, adjustments to the comparable data, and discussion of the reliability and credibility of the data as it relates to the indicated subject property value. Improved comparable sales which are used to compare to vacant land subject properties shall include an allocation between land and improvements, using methodology similar to methodology used in item 16 above to estimate improvement value, when possible, with an explanation of the methodology used.
26. Comparable data sheets.
 - a. For sales, include information on grantor/Grantee, sale/recordation dates, listed or asking price as of the date of sale, highest and best use, financing, conditions of sale, buyer motivation, sufficient location information (street address, post mile, and/or distance from local landmarks such as bridges, road intersections, structures, etc.), land/site characteristics, improvements, source of any allocation of sale price between land and improvements, and confirming source.
 - b. For listings, also include marketing time from list date to effective date of the appraisal, original list price, changes in list price, broker feedback, if available.

- c. For leases, include significant information such as lessor/lessee, lease date and term, type of lease, rent and escalation, expenses, size of space leased, tenant improvement allowance, concessions, use restrictions, options, and confirming source. When comparing improved sales to a vacant land subject, the contributory value of the improvements shall be segregated from the land value.
27. For appraisals of easements, a before and after analysis of the burden of the easement on the fee, with attention to how the easement affects highest and best use in the after condition. An Easement Valuation Matrix or generalized easement valuation references may be used ONLY as a reference for a secondary basis of value.
28. For partial taking and easement appraisals, valuation of the remainder in the after condition and analysis and identification of any change in highest and best use or other characteristics in the after condition, to establish severance damages to the remainder in the after condition, and a discussion of special and general benefits, and cost to cure damages or construction contract work.
29. There are occasions where properties involve water rights, minerals, or salable timber that require separate valuations. If an appraisal assignment includes water rights, minerals, or merchantable timber that requires separate valuation, the valuation of the water rights, minerals, or merchantable timber shall be completed by a credentialed subject matter specialist.
30. For partial taking and easement appraisals, presentation of the valuation in California partial taking acquisition required format.
31. Implied dedication statement.
32. Reconciliation and final value estimate. Include analysis and comparison of the comparable sales to the subject and explain and support conclusions reached.
33. Discussion of any departures taken in the development of the appraisal.
34. Signed Certification consistent with the language found in Uniform Standards of Professional Appraisal Practice.
35. If applicable, in addition to the above, appraisals of telecommunication sites shall also provide:
 - a. A discussion of market conditions and trends including identification of the relevant market, a discussion of supply and demand within the relevant market area and a discussion of the relevant market factors impacting demand for site acquisition and leasing within the relevant market area.
 - b. An analysis of other leases comparable to subject property. Factors to be discussed in the analysis include the latitude, longitude, type of tower, tower height, number of rack spaces, number of racks occupied, placement of racks, power source and adequacy, back-up power, vault and site improvements description and location on site, other utilities; access and road maintenance costs.

EXHIBIT K

INFORMATION NEEDED FOR ESCROW PROCESSING AND CLOSURE

The Grantee shall provide the following documents to the State Project Representative during the escrow process. Property acquisition escrow documents shall be submitted within the term of this Grant Agreement and after a qualified appraisal has been approved.

- Name and Address of Title Company Handling the Escrow
- Escrow Number
- Name of Escrow Officer
- Escrow Officer's Phone Number
- Dollar Amount Needed to Close Escrow
- Legal Description of Property Being Acquired
- Assessor's Parcel Number(s) of Property Being Acquired
- Copy of Title Insurance Report
- Entity Taking Title as Named Insured on Title Insurance Policy
- Copy of Escrow Instructions in Draft Form Prior to Recording for Review Purposes
- Copy of Final Escrow Instructions
- Verification that all Encumbrances (i.e., Liens, Back Taxes, and Similar Obligations) have been Cleared Prior to Recording the Deed to Transfer Title
- Copy of Deed for Review Purposes Prior to Recording
- Copy of Deed as Recorded in County Recorder's Office
- Copy of Escrow Closure Notice

EXHIBIT L

PROJECT MONITORING PLAN GUIDANCE

Introduction

For each project contained in Exhibit A, please include a brief description of the project (maximum ~150 words) including project location, implementation elements, need for the project (what problem will the project address) and responds to the requirements listed below.

Project Monitoring Plan Requirements

The Project Monitoring Plan shall contain responses to the following questions:

- What are the anticipated project physical benefits?
- What are the corresponding numeric targets for each project benefit?
- How will proposed numeric targets be measured?
- What are baseline conditions?
- When will the targets be met (e.g., upon project completion, five years after completion)?
- How often will monitoring be undertaken (e.g., monthly, yearly).
- Where are monitoring point locations (e.g., meter located at..., at stream mile...)? Include relevant maps.
- How will the project be maintained (e.g., irrigation, pest management, weed abatement)?
- What will be the frequency and duration of maintenance proposed activities?
- Are there any special environmental considerations (e.g., resource agency requirements, permit requirements, CEQA/NEPA mitigation measures)?
- Who is responsible for collecting the samples (i.e., who is conducting monitoring and/or maintenance)?
- How, and to whom, will monitoring results be reported (e.g., paper reports, online databases, public meetings)?
- What adaptive management strategies will be employed if problems are encountered during routine monitoring or maintenance?
- What is the anticipated life of the project?

EXHIBIT M

INVOICE GUIDANCE FOR ADMINISTRATIVE AND OVERHEAD CHARGES

The funds provided pursuant to this Agreement may only be used for costs that are directly related to the funded Project. The following provides a list of typical requirements for invoicing, specifically providing guidance on the appropriate methods for invoicing administrative and direct overhead charges.

Administration Charges

Indirect and General Overhead (i.e., indirect overhead) charges are not an allowable expense for reimbursement. However, administrative expenses that are apportioned directly to the project are eligible for reimbursement. Cost such as rent, office supplies, fringe benefits, etc. can be "Direct Costs" and are eligible expenses as long as:

- There is a consistent, articulated method for how the costs are allocated that is submitted and approved by the Grant Manager. The allocation method must be fully documented for auditors.
- A "fully-burdened labor rate" can be used to capture allowable administrative costs.
- The administrative/overhead costs can never include:
 - Non-project specific personnel and accounting services performed within the Grantee or an LPS' organization
 - Generic markup
 - Tuition
 - Conference fees
 - Building and equipment depreciation or use allowances
- Using a general overhead percentage is never allowed

Labor Rates

The Grantee must provide DWR with supporting documentation for personnel hours (see personnel billing rates letter in example invoice packet). The personnel rate letter should be submitted to the DWR Grant Manager prior to submittal of the first invoice. The supporting documentation must include, at a minimum, employee classifications that will be reimbursed by grant funds and the corresponding hourly rate range. These rates should be "burdened"; the burdened rate must be consistent with the Grantee's/Local Project Sponsors standardized allocation methodology. The supporting documentation should also provide an explanation of what costs make up the burdened rate and how those costs were determined. This information will be used to compare against personnel hours summary table invoice back up documentation. Periodic updates may be needed during the life of the grant which would be handled through a revised billing rate letter.
